

FY 2022 Reasonable Progress Update: April 30, 2022


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 146 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$109 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations

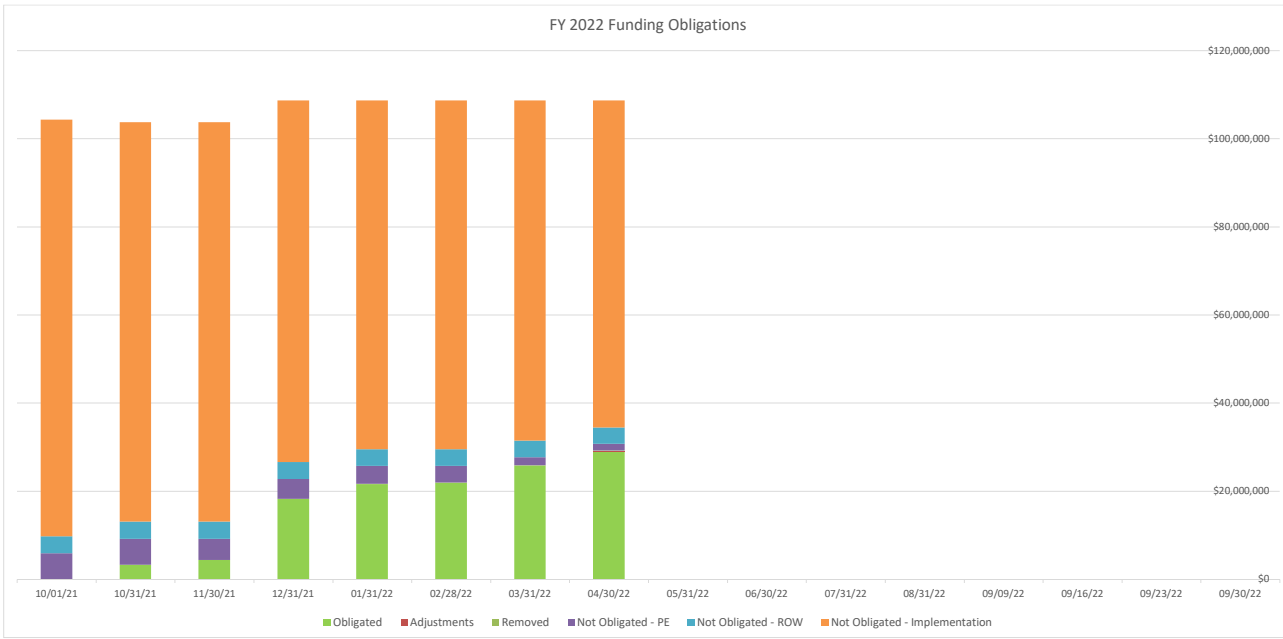

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	2	\$3,292,271	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
11/30/21	8	\$4,405,281	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
12/31/21	15	\$18,219,541	0	\$0	0	\$0	28	\$4,506,977	30	\$3,900,684	73	\$82,061,554	146	\$108,688,756
01/31/22	24	\$21,569,979	0	\$0	1	\$51,200	24	\$4,127,986	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
02/28/22	26	\$21,881,885	0	\$0	1	\$51,200	22	\$3,816,080	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
03/31/22	30	\$25,819,566	0	\$0	1	\$51,200	21	\$1,816,080	28	\$3,773,484	66	\$77,228,426	146	\$108,688,756
04/30/22	37	\$29,011,746	1	\$115,200	1	\$51,200	17	\$1,577,396	27	\$3,658,284	63	\$74,274,930	146	\$108,688,756
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$29,011,746	37 PROJECTS	
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22	10/01/2021
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22	10/01/2021
			October Total	\$3,292,271	2 Projects	
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
			November Total	\$1,113,010	6 Projects	
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21	12/07/2021
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21	12/07/2021
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Reestablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22	12/07/2021
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21	12/15/2021
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21	12/16/2021
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21	12/17/2021
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21	12/17/2021
			December Total	\$13,814,260	7 Projects	
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21	01/10/2022
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21	01/10/2022
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22	01/10/2022
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21	01/10/2022
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22	01/24/2022
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21	01/25/2022
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22	01/25/2022
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21	01/28/2022
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22	01/31/2022
			January Total	\$3,350,438	9 Projects	
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22	02/17/2022
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21	02/28/2022
			February Total	\$311,906	2 Projects	
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21	03/09/2022
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21	03/22/2022

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$29,011,746	37 PROJECTS	
Citizens For Modern Transit/BI-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20	03/23/2022
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21	03/28/2022
			March Total	\$3,937,681	4 Projects	
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21	04/01/2022
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22	04/01/2022
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21	04/08/2022
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout- Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21	04/21/2022
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21	04/21/2022
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22	04/21/2022
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22	04/29/2022
			April Total	\$3,192,180	7 Projects	
			May Total	\$0	0 Projects	
			June Total	\$0	0 Projects	
			July Total	\$0	0 Projects	
			August Total	\$0	0 Projects	
			September Total	\$0	0 Projects	

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$1,577,396	17 PROJECTS	
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$3,658,284		27 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delpont - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$74,274,930	63 PROJECTS	
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RRXing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Peruque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (BI 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$74,274,930		63 PROJECTS
St. Charles County	GGL- Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr. 20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Interctnt	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis		6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling; - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$74,274,930	63 PROJECTS	
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

Adjustments							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$115,200		1 PROJECTS		
		October Total	\$0		0 Projects		
		November Total	\$0		0 Projects		
		December Total	\$0		0 Projects		
		January Total	\$0		0 Projects		
		February Total	\$0		0 Projects		
		March Total	\$0		0 Projects		
		April Total	\$0		0 Projects		
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21	Sponsor using local funds for ROW	04/29/2022
		May Total	\$115,200		1 Projects		
		June Total	\$0		0 Projects		
		July Total	\$0		0 Projects		
		August Total	\$0		0 Projects		
		September Total	\$0		0 Projects		

Removed							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$51,200	1 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21	Sponsor removed project from TIP	01/04/2021
January Total			\$51,200	1 Projects			
February Total			\$0	0 Project			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2022 Reasonable Progress Update: March 31, 2022


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 145 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$108 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations

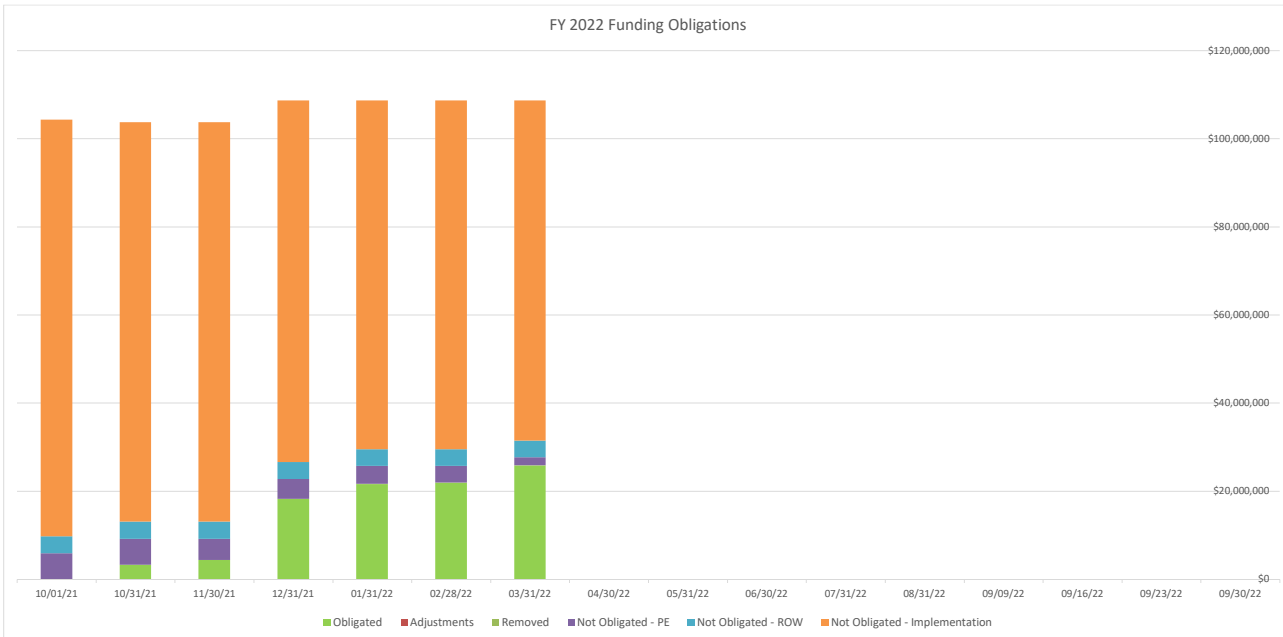

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	2	\$3,292,271	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
11/30/21	8	\$4,405,281	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
12/31/21	15	\$18,219,541	0	\$0	0	\$0	28	\$4,506,977	30	\$3,900,684	73	\$82,061,554	146	\$108,688,756
01/31/22	24	\$21,569,979	0	\$0	1	\$51,200	24	\$4,127,986	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
02/28/22	26	\$21,881,885	0	\$0	1	\$51,200	22	\$3,816,080	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
03/31/22	30	\$25,819,566	0	\$0	1	\$51,200	21	\$1,816,080	28	\$3,773,484	66	\$77,228,426	146	\$108,688,756
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$25,819,566	30 PROJECTS		
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22	10/01/2021
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22	10/01/2021
October Total			\$3,292,271	2 Projects		
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
November Total			\$1,113,010	6 Projects		
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21	12/07/2021
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21	12/07/2021
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Reestablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22	12/07/2021
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21	12/15/2021
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21	12/16/2021
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21	12/17/2021
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21	12/17/2021
December Total			\$13,814,260	7 Projects		
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21	01/10/2022
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21	01/10/2022
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22	01/10/2022
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21	01/10/2022
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22	01/24/2022
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21	01/25/2022
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22	01/25/2022
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21	01/28/2022
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22	01/31/2022
January Total			\$3,350,438	9 Projects		
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22	02/17/2022
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21	02/28/2022
February Total			\$311,906	2 Projects		
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21	03/09/2022
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21	03/22/2022

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$25,819,566		30 PROJECTS
Citizens For Modern Transit/Bi-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20	03/23/2022
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21	03/28/2022
			March Total	\$3,937,681		4 Projects
			April Total	\$0		0 Projects
			May Total	\$0		0 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September Total	\$0		0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$1,816,080	21 PROJECTS	
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
			TOTAL	\$3,773,484	28 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delpont - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$77,228,426		66 PROJECTS
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RR Xing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Peruque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$77,228,426	66 PROJECTS	
Pacific	West Osage Street (BI 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL- Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Interct	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling: - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$77,228,426	66 PROJECTS	
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

Removed							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$51,200	1 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21	Sponsor removed project from TIP	01/04/2021
January Total			\$51,200	1 Projects			
February Total			\$0	0 Project			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2022 Reasonable Progress Update: February 28, 2022


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 145 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$104 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations

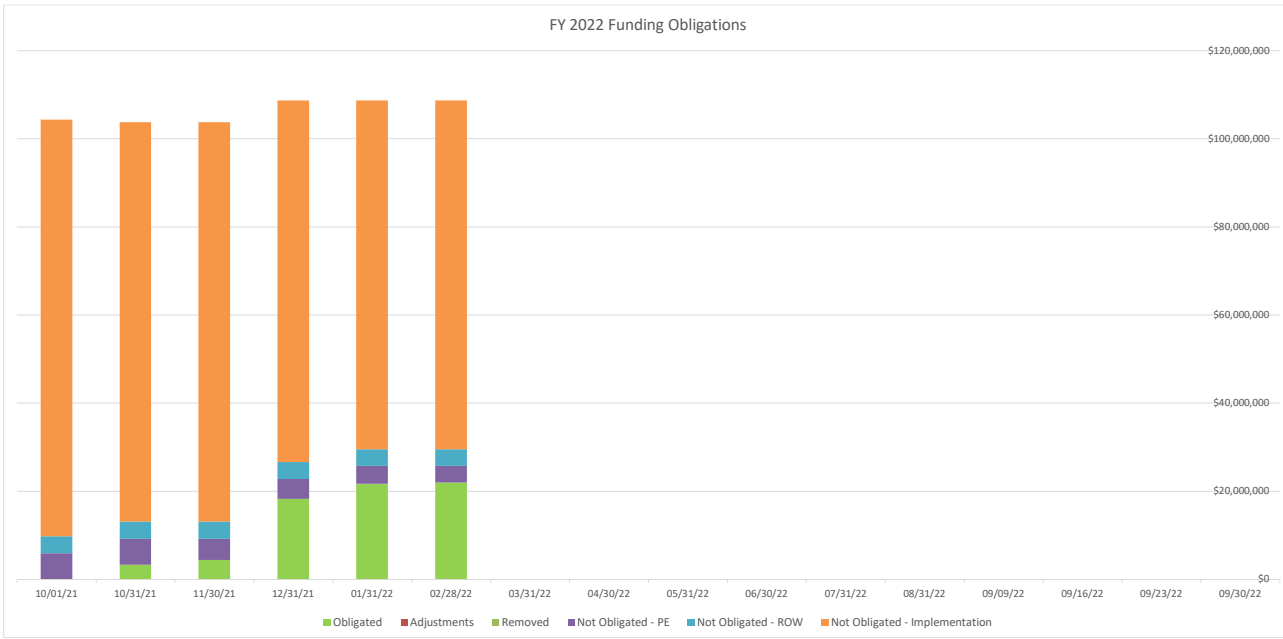

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	2	\$3,292,271	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
11/30/21	8	\$4,405,281	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
12/31/21	15	\$18,219,541	0	\$0	0	\$0	28	\$4,506,977	30	\$3,900,684	73	\$82,061,554	146	\$108,688,756
01/31/22	24	\$21,569,979	0	\$0	1	\$51,200	24	\$4,127,986	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
02/28/22	26	\$21,881,885	0	\$0	1	\$51,200	22	\$3,816,080	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
03/31/22														
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$21,881,885	26 PROJECTS	
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22	10/01/2021
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22	10/01/2021
			October Total	\$3,292,271	2 Projects	
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
			November Total	\$1,113,010	6 Projects	
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21	12/07/2021
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21	12/07/2021
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Reestablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22	12/07/2021
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21	12/15/2021
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21	12/16/2021
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21	12/17/2021
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21	12/17/2021
			December Total	\$13,814,260	7 Projects	
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21	01/10/2022
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21	01/10/2022
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22	01/10/2022
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21	01/10/2022
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22	01/24/2022
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21	01/25/2022
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22	01/25/2022
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21	01/28/2022
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22	01/31/2022
			January Total	\$3,350,438	9 Projects	
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22	02/17/2022
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21	02/28/2022
			February Total	\$311,906	2 Projects	
			March Total	\$0	0 Projects	
			April Total	\$0	0 Projects	

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$21,881,885	26 PROJECTS	
		May Total		\$0	0 Projects	
		June Total		\$0	0 Projects	
		July Total		\$0	0 Projects	
		August Total		\$0	0 Projects	
		September Total		\$0	0 Projects	

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$3,816,080	22 PROJECTS	
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
			TOTAL	\$3,773,484	28 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delpont - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$79,166,107	69 PROJECTS	
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Citizens For Modern Transit/Bi-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RR Xing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Perouque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co.; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$79,166,107	69 PROJECTS	
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (Bl 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL- Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$79,166,107		69 PROJECTS
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

Adjustments							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$0	0 PROJECTS			
	October Total		\$0	0 Projects			
	November Total		\$0	0 Projects			
	December Total		\$0	0 Projects			
	January Total		\$0	0 Projects			
	February Total		\$0	0 Projects			
	March Total		\$0	0 Projects			
	April Total		\$0	0 Projects			
	May Total		\$0	0 Projects			
	June Total		\$0	0 Projects			
	July Total		\$0	0 Projects			
	August Total		\$0	0 Projects			
	September Total		\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$51,200		1 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21	Sponsor removed project from TIP	01/04/2021
January Total			\$51,200		1 Projects		
February Total			\$0		0 Project		
March Total			\$0		0 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2022 Reasonable Progress Update: January 31, 2022


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 146 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$109 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations

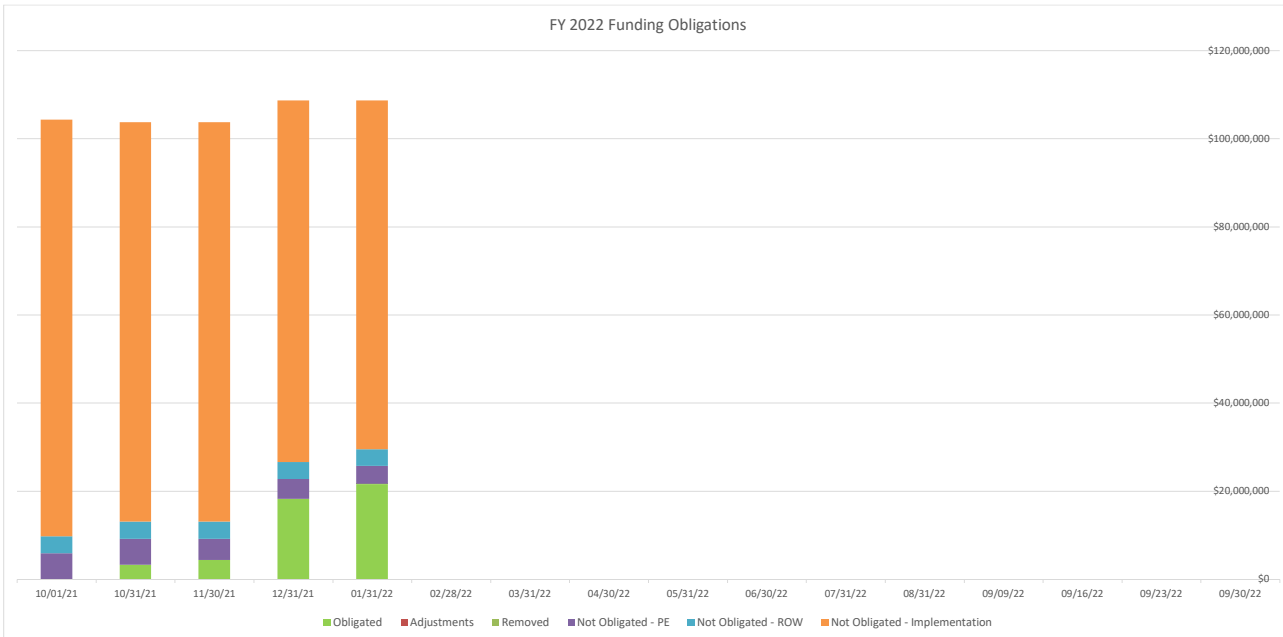

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	2	\$3,292,271	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
11/30/21	8	\$4,405,281	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
12/31/21	15	\$18,219,541	0	\$0	0	\$0	28	\$4,506,977	30	\$3,900,684	73	\$82,061,554	146	\$108,688,756
01/31/22	24	\$21,569,979	0	\$0	1	\$51,200	24	\$4,127,986	28	\$3,773,484	69	\$79,166,107	146	\$108,688,756
02/28/22														
03/31/22														
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$21,569,979	24 PROJECTS	
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22	10/01/2021
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22	10/01/2021
			October Total	\$3,292,271	2 Projects	
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
			November Total	\$1,113,010	6 Projects	
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21	12/07/2021
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21	12/07/2021
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Restablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22	12/07/2021
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21	12/15/2021
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21	12/16/2021
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21	12/17/2021
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21	12/17/2021
			December Total	\$13,814,260	7 Projects	
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21	01/10/2022
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21	01/10/2022
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22	01/10/2022
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21	01/10/2022
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22	01/24/2022
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21	01/25/2022
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22	01/25/2022
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21	01/28/2022
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22	01/31/2022
			January Total	\$3,350,438	9 Projects	
			February Total	\$0	0 Projects	
			March Total	\$0	0 Projects	
			April Total	\$0	0 Projects	

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$21,569,979	24 PROJECTS	
			May Total	\$0	0 Projects	
			June Total	\$0	0 Projects	
			July Total	\$0	0 Projects	
			August Total	\$0	0 Projects	
			September Total	\$0	0 Projects	

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$4,127,986	24 PROJECTS	
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
			TOTAL	\$3,773,484	28 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delpont - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$79,166,107	69 PROJECTS	
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Citizens For Modern Transit/BI-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RR Xing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Perouque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co.; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$79,166,107	69 PROJECTS	
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (Bl 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL- Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$79,166,107		69 PROJECTS
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

Removed							
Sponsor	Title - Description	TIP #	FY 2021	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$51,200		1 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21	Sponsor removed project from TIP	01/04/2021
January Total			\$51,200		1 Projects		
February Total			\$0		0 Project		
March Total			\$0		0 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2022 Reasonable Progress Update: December 31, 2021

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 146 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$108 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	2	\$3,292,271	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
11/30/21	8	\$4,405,281	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	76	\$90,627,554	145	\$103,688,756
12/31/21	15	\$18,219,541	0	\$0	0	\$0	28	\$4,506,977	30	\$3,900,684	73	\$82,061,554	146	\$108,688,756
01/31/22														
02/28/22														
03/31/22														
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$18,219,541			15 PROJECTS
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22	10/01/2021
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22	10/01/2021
October Total			\$3,292,271			2 Projects
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
November Total			\$1,113,010			6 Projects
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21	12/07/2021
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21	12/07/2021
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Restablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22	12/07/2021
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21	12/15/2021
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21	12/16/2021
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21	12/17/2021
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21	12/17/2021
December Total			\$13,814,260			7 Projects
January Total			\$0			0 Projects
February Total			\$0			0 Projects
March Total			\$0			0 Projects
April Total			\$0			0 Projects
May Total			\$0			0 Projects
June Total			\$0			0 Projects
July Total			\$0			0 Projects
August Total			\$0			0 Projects
September Total			\$0			0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$4,506,977	28 PROJECTS	
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$3,849,484	29 PROJECTS	
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delpport - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22

Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21
------------	---	---------	----------	-----	--------

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$82,061,554	73 PROJECTS	
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Citizens For Modern Transit/Bi-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RRXing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Perouque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co.; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$82,061,554		73 PROJECTS
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (BI 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles	Zumbel Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL- Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Interctnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$82,061,554		73 PROJECTS
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling: - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

FY 2022 Reasonable Progress Update: November 30, 2021

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 145 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$104 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE	ROW	CONST	PE	ROW	CONST	#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	78	\$93,919,825	145	\$103,688,756
11/30/21	6	\$1,113,010	0	\$0	0	\$0	31	\$4,755,237	30	\$3,900,684	78	\$93,919,825	145	\$103,688,756
12/31/21														
01/31/22														
02/28/22														
03/31/22														
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
TOTAL #REF!						6 PROJECTS
October Total			\$0	0 Projects		
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21	11/05/2021
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21	11/05/2021
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21	11/05/2021
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21	11/05/2021
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21	11/05/2021
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21	11/15/2021
November Total			\$1,113,010	6 Projects		
December Total			\$0	0 Projects		
January Total			\$0	0 Projects		
February Total			\$0	0 Projects		
March Total			#REF!	0 Projects		
April Total			\$0	0 Projects		
May Total			\$0	0 Projects		
June Total			\$0	0 Projects		
July Total			#REF!	0 Projects		
August Total			\$0	0 Projects		
September Total			\$0	0 Projects		

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$4,755,237	31 PROJECTS	
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$4,755,237		31 PROJECTS
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$3,900,684	30 PROJECTS	
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delport - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22

Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$93,919,825		78 PROJECTS
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Citizens For Modern Transit/Bi-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RRXing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Peruque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$93,919,825	78 PROJECTS	
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (BI 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Restablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$93,919,825	78 PROJECTS	
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22

FY 2022 Reasonable Progress Update: October 31, 2021

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 145 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2022 of the FY 2022-2025 Transportation Improvement Program (TIP). These projects, sponsored by 53 different agencies and representing \$104 million in federal funds, are subject to a September 30, 2022 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MODOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2022. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2022 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE	ROW	CONST	PE	ROW	CONST	#	Federal \$
10/01/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	79	\$94,549,825	146	\$104,318,756
10/31/21	0	\$0	0	\$0	0	\$0	37	\$5,868,247	30	\$3,900,684	78	\$93,919,825	145	\$103,688,756
11/30/21														
12/31/21														
01/31/22														
02/28/22														
03/31/22														
04/30/22														
05/31/22														
06/30/22														
07/31/22														
08/31/22														
09/09/22														
09/16/22														
09/23/22														
09/30/22														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2021	Phase	Scheduled Obligation	Actual Obligation
TOTAL #REF!						0 PROJECTS
October Total			\$0			0 Projects
November Total			\$0			0 Projects
December Total			\$0			0 Projects
January Total			\$0			0 Projects
February Total			\$0			0 Projects
March Total		#REF!				0 Projects
April Total			\$0			0 Projects
May Total			\$0			0 Projects
June Total			\$0			0 Projects
July Total		#REF!				0 Projects
August Total			\$0			0 Projects
September Total			\$0			0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$5,868,247	37 PROJECTS	
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$172,000	PE	Dec-21
Dardenne Prairie	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd - Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$25,138	PE	Apr-21
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$31,906	PE	Jun-22
Fenton	Old Highway 141 - Gravois Rd To County Line - Resurfacing - Curb Ramps	7109-22	\$40,000	PE	Nov-21
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St To N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$76,000	PE	Oct-21
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Manor Ln - Resurfacing - Sidewalk (6')	7112-22	\$112,280	PE	Oct-21
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 - Ada Compliance - Exterior - Platform Cover	7158-22	\$117,188	PE	Apr-22
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$101,040	PE	Nov-21
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$96,160	PE	Nov-21
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$12,000	PE	Apr-21
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge - Sidewalks (6')	7159-22	\$84,000	PE	Dec-21
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail To Middle School - Shared Use Path (10')	7160-22	\$21,951	PE	Nov-21
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$85,610	PE	Sep-22
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$96,000	PE	Mar-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$91,324	PE	Mar-21
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$88,480	PE	May-21
Pine Lawn	Natural Bridge (Mo 115) Sidewalks - Dardenne Ave To Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$86,364	PE	May-22
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$47,200	PE	Oct-21
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$280,000	PE	Oct-21
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$80,000	PE	Dec-21
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd - Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$186,000	PE	May-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd To Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$94,800	PE	Apr-21
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink - Design For Bridge Replacement	7123A-22	\$2,000,000	PE	Oct-21
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd - Cycle Track (10') - Curb Ramps	7213-22	\$120,000	PE	Jan-21
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$104,000	PE	Nov-21
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr - Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$138,400	PE	Oct-21
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) - Resurfacing - Curb Ramps	7124B-22	\$179,440	PE	Oct-21
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$39,820	PE	Dec-21

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$5,868,247	37 PROJECTS	
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) - Resurfacing - Curb Ramps	7124C-22	\$118,000	PE	Oct-21
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. B	7124G-22	\$422,800	PE	Oct-21
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd - Resurfacing - Curb Ramps	7124D-22	\$146,050	PE	Oct-21
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl - Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$108,320	PE	Oct-21
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$48,216	PE	Mar-21
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$86,400	PE	Oct-21
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$55,360	PE	Jan-22
Wildwood	MO 109 - At MO Ba (South) - Roundabout - Shared Use Path (10')	7129-22	\$148,000	PE	Nov-21
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr - Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$128,000	PE	Oct-21

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$3,900,684	30 PROJECTS	
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$20,000	ROW	Feb-22
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau;Russell-Bw-Bremerton - Shared Use Path(12' Bw,8' Russ), Sidewalk	7154-22	\$68,000	ROW	Jan-22
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd To Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$144,000	ROW	Nov-21
Creve Coeur	North New Ballas Sidewalk - Rocky Dr To 315' S/O Magna Carta Dr - Sidewalk	7155-22	\$4,000	ROW	Dec-21
Dardenne Prairie	Stump Road - Feise Rd To MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$16,000	ROW	Oct-21
Fenton	Larkin Williams Road - South Highway Dr To Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$16,000	ROW	Feb-22
Franklin County	Hendricks Road Bridge - Over North Fork Of Meramec River - Replace Bridge	6948-21	\$18,000	ROW	Apr-22
Glendale	E. Essex Avenue - Sappington Rd To Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$38,600	ROW	May-22
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd - Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$46,000	ROW	Oct-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$19,200	ROW	Jan-22
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$63,000	ROW	Aug-23
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$36,000	ROW	Jan-22
Jefferson County	Laguna Palma Road & Mcgehan Road Bridges - Over Boyd Branch & Tributary Of Joachim Creek - Replace Bridges	6952C-21	\$38,400	ROW	Jan-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl To Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$248,284	ROW	Jan-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$213,600	ROW	Oct-21
Ladue	Dielman Road - Tamarack Dr To Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$76,000	ROW	Oct-21
Ladue	Warson Road - At Conway Rd - Traffic Signal - Left Turn Lane	7130-21	\$51,200	ROW	Oct-21
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$30,000	ROW	Oct-21
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail To 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$66,000	ROW	Dec-21
Manchester	Manchester Rd (Mo 100) Sidewalk - Baxter Rd To MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$156,400	ROW	Mar-22
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad - Replace SW Bridge - Realign Columbia To SW	6502B-22	\$1,440,000	ROW	Oct-21
St. Louis County	Mason Road - 2022 - Clayton Rd To 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$115,200	ROW	Jun-21
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lns - Traffic Signal	7139-21	\$40,000	ROW	Sep-22
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$639,800	ROW	Jun-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) To Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$72,000	ROW	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page To Midland; Midland: N/S To Delport - Sidewalks (5-6')	6752A-21	\$80,000	ROW	Dec-21
Washington	Jefferson Street - Fifth St To MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$20,000	ROW	Jan-22
Washington	Westlink Drive - Bluff Rd To W. Main St. - Overlay - Improve Intersection At Bluff Rd	6971-21	\$40,000	ROW	Jan-22

Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr To 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$10,000	ROW	Jun-22
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$75,000	ROW	Dec-21

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
TOTAL			\$93,919,825		78 PROJECTS
Ballwin	New Ballwin Road - Manchester Rd (Mo 100) To Twigwood Dr - Resurfacing - Curb Ramps	6938-22	\$652,863	CONST	Dec-21
Citizens For Modern Transit/Bi-State	Building Ridership On Transit - Stl City And Stl County - Education & Outreach Building - Better Bus Stops- New Fare Media - Employer Benefit Program	7202-22	\$432,351	CONST	Oct-20
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr To - Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
Creve Coeur	Mosley Road, Phase 1 - Tureen Dr To Olive Blvd (MO 340) - Resurfacing - Curb Ramps	6896-21	\$676,000	CONST	Oct-21
De Soto	Boyd Street Sidewalk - MO 21 To Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
De Soto	N. Main St, Phase 1 - Skyline Dr To Valley Pl - Resurfacing - Sidewalk (6') - Lighting	6942-22	\$652,243	CONST	Dec-21
Des Peres	Des Peres Road - At Old Des Peres Rd - Roundabout - Sidewalk	6976-20	\$1,163,496	CONST	Nov-22
Des Peres	MO 100 (Manchester Road) Improvements - Ballas Rd To Meier Ln - Access Management - Crosswalk Impr. - Bus Stop Impr	6897-20	\$267,640	IMPL	Oct-21
Edmundson	Edmundson Road - Natural Bridge To Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Eureka	Allenton Bridge, Phase 1 - Over Union Pacific Railroad - Replace Bridge - Shared Use Path (8')	6898-22	\$1,928,080	CONST	Oct-21
Fenton	Rudder Road - Larkin Williams Rd To 200' E/O Fenton Business Ct - Reconstruction - Sidewalk (5')	6912-20	\$1,119,102	CONST	Dec-21
Festus	S. Mill Street - Main St To Veterans Blvd (MO A) - Overlay - Lighting - Sidewalk (Lee To N. Creek - 5')	6908-22	\$496,432	CONST	Jan-22
Festus	W. Main Street, Phase 1 - Park Ave To Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St To N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	Elmont Road - Over Little Boone Creek - Replace Bridge	6906-20	\$572,835	CONST	Dec-21
Frontenac	Geyer Road, Phase 1 - Clayton Rd To Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,394,538	CONST	Dec-21
Jefferson County	High Ridge Blvd Sidewalk - Crossroads Plaza Ent. To Park Rd - Sidewalk (7') - Lighting - Xing At Community Ln	7157-22	\$1,079,370	CONST	Apr-22
Jefferson County	Hillsboro House Springs Road Bridge - Over Bourne Creek - Replace Bridge	6913D-20	\$691,166	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Ln - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County Port Authority	Marine Vessel Engine Repower - 2022 - Repower One Marine Vessel Serving Mississippi - River In Non-Attainment Area - 1 Towboat	6977A-22	\$269,500	CONST	Jul-21
Kirkwood	Geyer Road, Phase 2 - West Adams Ave To 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct Rd At Up RRXing	6917-22	\$1,139,635	CONST	Aug-22
Lake Saint Louis	Lake Saint Louis Blvd, Phase 3 - Blue Cove Terrace To Peruque Creek Bridge - Reconstruction - Turn Ln At Bent Oak Dr/Bent Oak Cutoff	6955-22	\$950,000	CONST	Mar-22
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Maplewood	Manchester Road - Big Bend Blvd To City Limits (150' E/O Yale Ave) - Resurfacing - Curb Ramps - Mid-Block Xing	6902-20	\$1,160,000	CONST	Nov-21
Maryland Heights	Fee Fee Road - Schuetz Rd To Westport Plaza Dr - Slab Replacement - Diamond Grind - Bridge Deck	6903-22	\$630,000	CONST	May-22
MoDOT	I-70 - At MO 94 (First Capitol Dr) - Interchange Improvements	6979A-20	\$2,088,596	CONST	Jun-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$93,919,825	78 PROJECTS	
MoDOT	MO 94 - Sherman Dr To Pralle Ln - Widen To Six Lanes	7122B-23	\$1,203,675	CONST	Oct-22
MoDOT	Signal Optimization - 2022 - Various Locations Along MO 180, MO 21, MO N, MO U, MO EE - & MO 267 In St. Louis Co; US 61/67 In Jeff Co.; MO K In St. Charles Co	6979C-22	\$568,000	CONST	Aug-22
Oak Grove Village	E. Springfield Rd - MO 185 To North City Limits - Resurfacing - Shoulders (6')	6957-22	\$505,330	CONST	Dec-21
O'Fallon	Main St, Phase 1 - Pitman St To S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	IMPL	Dec-21
Pacific	Congress St (Former Rte N) - Westlake Village Dr To Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Ln (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	Denton Road Bridge - Over Brush Creek - Replace Bridge - Sidewalk (6')	6914-20	\$997,230	CONST	Oct-21
Pacific	West Osage Street (BI 44) - Noonan Plaza To I-44 Off Ramp; Western Ave To Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Ann	Geraldine Avenue Bridge - Over Coldwater Creek - Replace Bridge - Sidewalk (5')	6911-20	\$468,000	CONST	Dec-22
St. Charles	Boschertown Road, Phase 2 - Hecker St To MO B - Reconstruction - Shared Use Path (8') - TWTL (Locally Funded)	6922A-22	\$1,000,000	CONST	Oct-21
St. Charles	Zumbehl Rd - Over Cole Creek - Replace Culvert - Shared Use Path (10') - Sidewalk (5')	6922B-20	\$1,632,000	CONST	Jun-22
St. Charles County	Central School Road - At St. Peters Howell Rd - Intersection Improvements	6981A-22	\$1,000,000	CONST	Dec-21
St. Charles County	Gateway Green Light, Phase 6 - Various Rds In St. Charles Co - Ptz Cameras, Travel - Time Detectors, Fiber, Atms - Signal Opt. - Emer. Veh. Preempt	6841A-19	\$790,074	CONST	Sep-22
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy - Signal Perf. Module - Bryan: W. Terra Ln To MO N; Wentzville Pkwy Veterans Mem Pkwy To US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd To S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd To Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd To E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	MO N - At MO Z - Traffic Signal - Realign Intersection	6847-19	\$1,110,000	CONST	Sep-22
St. Charles County	MO N - Mothershead Rd To Mid Rivers Mall Dr - Resurfacing - Sidewalk (5')	6924-22	\$1,130,000	CONST	Oct-21
St. Charles County	Smart Parking Management System - Dt St. Charles - Develop Smart Parking System - Parking Lot Sensors - Msg Signs - Cameras - Phone App - Lease Electric Shuttle	6981C-20	\$800,000	CONST	Sep-22
St. Clair	Kitchell Avenue - Commercial Ave To Main St - Resurfacing - Sidewalks (5' S. Side/6' N. Side)	6909-22	\$299,015	CONST	Jan-22
St. Louis	Jefferson / 22nd Traffic Flow Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Signal Improvements - Shared Use Path/Cycle Track	6919A-19	\$6,720,000	CONST	Sep-21
St. Louis	Jefferson Avenue, Phase 1 - Market St To Cass Ave - Resurfacing - Sidewalks Impr. (6') - Ln Reduct. 6 To 4	6849A-23	\$7,125,000	CONST	Nov-22
St. Louis	Jefferson/22nd St Interchange Improvements - Reconfigure I-64/Pine/Market/Jefferson Interchange - Restablish Street Grid - Curb Ramps - Resurfacing	6919AA-21	\$5,040,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various Locations Along Goodfellow, MLK Dr, Halls - Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis County	Airport Rd - E/O I-170 To N Florissant Rd - Resurfacing - Curb Ramps	6745J-21	\$2,105,460	CONST	Sep-22
St. Louis County	Bayless Avenue - 2020 - Union Rd To Lemay Ferry Rd - Resurfacing	6745B-19	\$1,316,080	CONST	Sep-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation
		TOTAL	\$93,919,825	78 PROJECTS	
St. Louis County	Bayless Avenue Bridge - Over Gravois Creek (Approx 130' East Of I-55) - Replace Bridge - Sidewalk (6')	6834B-21	\$2,100,000	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 To Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Creve Coeur Mill Road - 2021 - Prichard Farm Rd To Approx 350' W/O Mckelvey Rd. - Resurfacing - Slab Replacement - Fiberoptic	6834D-21	\$1,100,000	CONST	Sep-22
St. Louis County	Hanley Road - 2021 - Canton Rd To MO D (Page Ave) - Resurfacing	6834E-21	\$1,100,000	CONST	Sep-22
St. Louis County	Heintz Road Bridge - Over Mattese Creek - Replace Bridge - Sidewalk (6')	6905B-20	\$1,164,800	IMPL	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Olive Blvd (MO 340) To Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	McKelvey Rd/Bennington Pl/Ameling Rd - 2021 - McKelvey/Bennington - Dorsett To Ameling; Ameling - Bennington To McKelvey - Resurfacing - Slab Repl.	6834C-21	\$1,000,000	CONST	Sep-22
St. Louis County	McKelvey Road, Phase 2 - 2021 - Glenpark Dr To Creve Coeur Mill Rd - Resurfacing - Sidewalk (5') E: Smoke Rise To Cr. Coeur Mill	6834F-19	\$921,480	CONST	Sep-22
St. Louis County	Meramec Bottom Road Bridge - Over Lemay Creek (Approx 1200' West Of I-55) - Replace Bridge	6834G-19	\$930,560	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd To North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd To Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr To Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd To City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Washington Street - 2021 - Rue St. Pierre To Fatima Ct - Resurfacing	6834H-21	\$1,100,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr To Manchester Rd (MO 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Peters	MO 370 - At Salt River Road, Phase 1 - New Interchange - Wb And Sb	6964-22	\$945,000	CONST	Dec-21
Union	N. Oak Street - E. Springfield Ave To US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
University City	Canton Avenue, Phase 1 - North & South Rd To N. Hanley Rd - Resurfacing - Sidewalks (6')	6969-21	\$672,728	CONST	May-22
University City	Westgate Ave - Delmar Blvd To MO 340 (Olive Blvd) - Resurfacing - Upgrade Sidewalk	6838-19	\$811,274	CONST	Sep-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 To 3rd St - Reconstruct: Rr To 3rd; Resurf: Rr To 141 - Sidewalks (5')	6918-20	\$1,288,553	CONST	Aug-22
Washington	Third Street - MO 47 To Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Add Nb Right Turn Lane	6984-20	\$137,927	CONST	Jan-22
Wentzville	Wentzville Parkway/I-70, Phase 1 - Wentzville Pkwy: Pearce To Veterans Mem - Relocate - I-70 Wb On Ramp - Roundabout	6933A-19	\$1,767,613	CONST	Sep-22
