

FY 2023 Reasonable Progress Update: September 16, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 189 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 51 different agencies and representing \$137 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

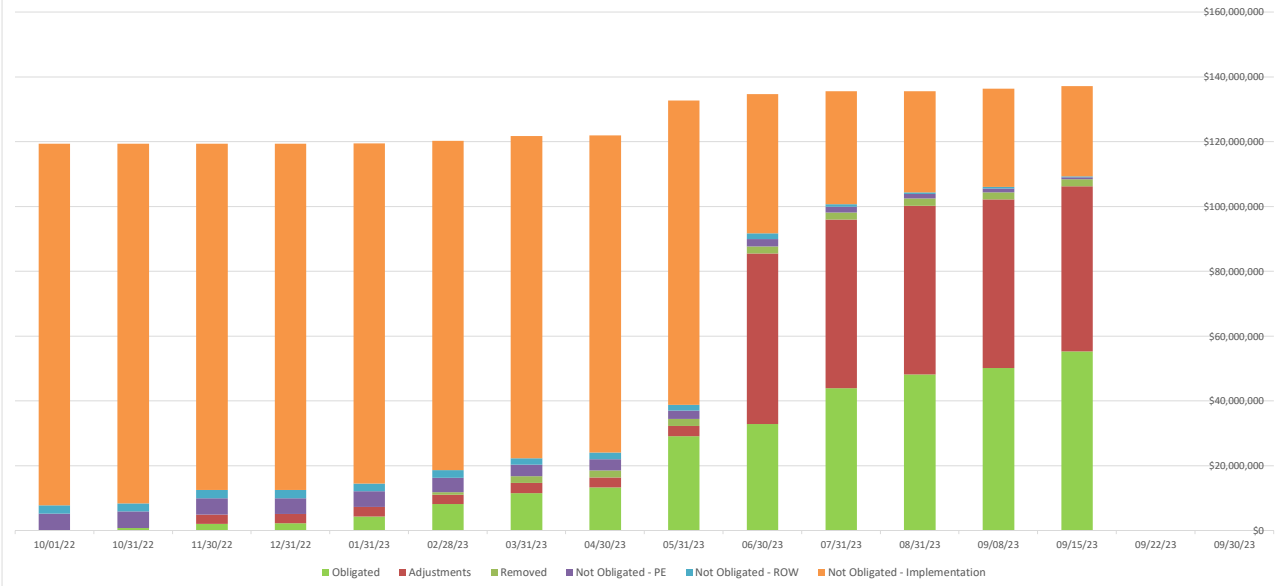

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23	52	\$29,210,065	7	\$3,097,069	2	\$2,160,000	17	\$2,577,687	20	\$1,771,206	79	\$93,923,975	177	\$132,740,002
06/30/23	62	\$32,935,192	43	\$52,596,382	2	\$2,160,000	15	\$2,352,167	20	\$1,771,006	41	\$42,910,827	183	\$134,725,574
07/31/23	83	\$43,955,847	46	\$52,050,562	3	\$2,215,200	8	\$1,755,390	11	\$758,384	33	\$34,907,151	184	\$135,642,534
08/31/23	94	\$48,253,136	46	\$52,050,562	3	\$2,215,200	6	\$1,377,578	7	\$502,384	28	\$31,243,674	184	\$135,642,534
09/08/23	100	\$50,184,540	46	\$52,050,562	3	\$2,215,200	5	\$1,194,774	6	\$449,884	27	\$30,326,945	187	\$136,421,905
09/15/23	111	\$55,346,801	45	\$50,893,672	3	\$2,215,200	3	\$582,222	3	\$303,700	24	\$27,871,097	189	\$137,212,692
09/22/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$48,253,136		94 PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/01/2022
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/05/2022
			October Total	\$880,270		2 Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7133-23	\$1,224,000	CONST	Nov-22	11/30/2022
			November Total	\$1,224,000		1 Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/2022
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/2022
			December Total	\$216,000		2 Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Jul-23	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Sep-23	01/09/2023
			January Total	\$2,130,892		5 Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Sep-23	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Dec-22	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
			February Total	\$3,772,393		8 Projects
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Sep-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Jul-23	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
			March Total	\$3,401,900		14 Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23	04/26/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jul-23	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brookling Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
			April Total	\$1,712,714		3 Projects
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(A) - Replace Nine Vans	7232A-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(B) - Replace Nine Vans	7232B-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(A) - Replace Ten Buses	7232C-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(B) - Replace Ten Buses	7232D-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22	05/02/2023
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23	05/31/2023
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Jul-23	05/02/2023
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22	05/02/2023
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23	05/01/2023
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23	05/31/2023
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$349,065	CONST	Oct-24	05/09/2023
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22	05/30/2023
St. Charles	Zumbehl Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Apr-23	05/10/2023
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23	05/30/2023
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22	05/30/2023
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jul-23	05/18/2023
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23	05/30/2023
			May Total	\$15,871,896		17 Projects
Arnold	Pomme Rd - Lonedell Rd to Rockview Ln - Reconstruction, Sidewalk	7268-24	\$299,801	PE	Nov-23	06/15/2023
Bi-State Development/Metro	Wabash Station Planning - Planning For Future Uses at Wabash Station near Delmar MetroLink Station	7268-24	\$400,000	IMPL	Nov-23	06/01/2023
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Sep-23	06/13/2023
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22	06/05/2023
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22	06/05/2023
St. Louis County	Dorsett Rd - 2026 - Marine to Calamaide - Resurfacing - Upgrade Sidewalks	7247B-24	\$289,500	PE	Nov-23	06/21/2023
St. Louis County	Hawkins Rd/New Sugar Creek Rd - Resurfacing, Shared Use Path	7247D-24	\$274,596	PE	Nov-23	06/28/2023
St. Louis County	Hanley Rd - 2026 - Dale Ave to Bruno Ave - Resurfacing, Sidewalk Upgrades	7247C-24	\$203,280	PE	Nov-23	06/01/2023
St. Louis County	Jennings Station/Chain of Rocks Rd - Halls Ferry Rd to St. Louis City Limit - Resurfacing, Shared Use Path, Upgrade Sidewalks	7247F-24	\$518,595	PE	Nov-22	06/21/2023
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22	06/20/2023
			June Total	\$3,725,127		10 Projects

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$48,253,136		94 PROJECTS
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23	07/05/2023
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23	07/13/2023
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23	07/25/2023
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Sep-23	07/27/2023
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22	07/15/2023
Jefferson County	Mt Olive Rd Bridge Over McMullen Branch - Replace Bridge	7113C-23	\$916,960	CONST	Oct-23	07/31/2023
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Sep-23	07/11/2023
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22	07/31/2023
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Sep-23	07/17/2023
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23	07/31/2023
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22	07/18/2023
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23	07/31/2023
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23	07/13/2023
St. Charles County	Zumbehl/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23	07/27/2023
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-23	07/31/2023
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22	07/27/2023
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22	07/31/2023
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Sep-23	07/17/2023
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23	07/17/2023
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22	07/24/2023
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23	07/12/2023
			July Total	\$11,020,655		21 Projects
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23	08/31/2023
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Sep-23	08/04/2023
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22	08/16/2023
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface - TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23	08/30/2023
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23	08/22/2023
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23	08/02/2023
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23	08/23/2023
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Sep-23	08/11/2023
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22	08/23/2023
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23	08/21/2023
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Sep-23	08/23/2023
			August Total	\$4,297,289		11 Projects
Arnold	Missouri State Rd Shared Use Path - Sherwood E.S. To Ridgeway Dr	7267-24	\$74,400	PE	Nov-23	09/05/2023
Breckenridge Hills	Isolda Ave Bridge - Over Coldwater Creek - Replace Bridge - Shoulders (4') - Sidewalk (4')	7104-22	\$495,034	CONST	Nov-23	09/05/2023
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22	09/05/2023
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22	09/01/2023
St. Louis County	Pennsylvania Avenue, Phase 1 - 2026 - Page Ave (MO D) to St. Charles Rock Rd (MO 180) - Resurfacing - Lane Reduction (4 to 2) - Upgrade Sidewalks	7247H-24	\$209,937	PE	Nov-23	09/05/2023
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22	09/01/2023
			September 8, 2023 Total	\$1,931,404		6 Projects
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Sep-23	09/12/2023
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22	09/14/2023
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22	09/13/2023
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23	09/11/2023
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22	09/12/2023
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22	09/11/2023
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	Apr-23	09/13/2023
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Sep-23	09/11/2023
St. Louis County	Big Bend Blvd-2026 - Elm Avenue to I-44 - Resurfacing, Sidewalk Upgrades, Ln Reduction	7247A-24	\$181,600	PE	Oct-23	09/11/2023
St. Louis County	Howdershell Road - 2026 - I-270 to 100' N/O Utz Ln - Resurfacing - Upgrade Sidewalks - Signal Impr.	7247E-24	\$609,187	PE	Oct-23	09/13/2023
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22	09/11/2023
			September 15, 2023 Total	\$5,162,261		11 Projects
			September 22, 2023 Total	\$0		0 Projects
			September 30, 2023 Total	\$0		0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$582,222	3 PROJECTS	
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL \$303,700 3 PROJECTS					
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$27,871,097		24 PROJECTS
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Sep-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Oct-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Sep-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Sep-23
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Sep-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Sep-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Sep-23
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Sep-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-23
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-23
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-23
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-23
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-23
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-23
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Sep-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$50,893,672	45 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2022
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23	EWG staff approved three-month schedule ext.	06/28/2023
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22	Board approved nine-month schedule ext.	06/28/2023
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22	EWG staff approved three-month schedule ext.	06/28/2023
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles County	Duelo Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
		June Total	\$47,024,103	34 Projects			
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23	MoDOT used ROW funds from 6S3416 - MoDOT resurfacing project on MO 115 - Shift ROW funds to construction	07/18/2023
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23	Coordination with adjacent MoDOT project design - shift ROW funds to construction	07/18/2023
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
		July Total	\$772,500	4 Projects			
		August Total	\$0	0 Projects			
		September Total	\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$2,215,200	3 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000	1 Project			
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000	1 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22	Project behind schedule	\$45,135
July Total			\$55,200	1 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2023 Reasonable Progress Update: August 31, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 184 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 50 different agencies and representing \$136 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

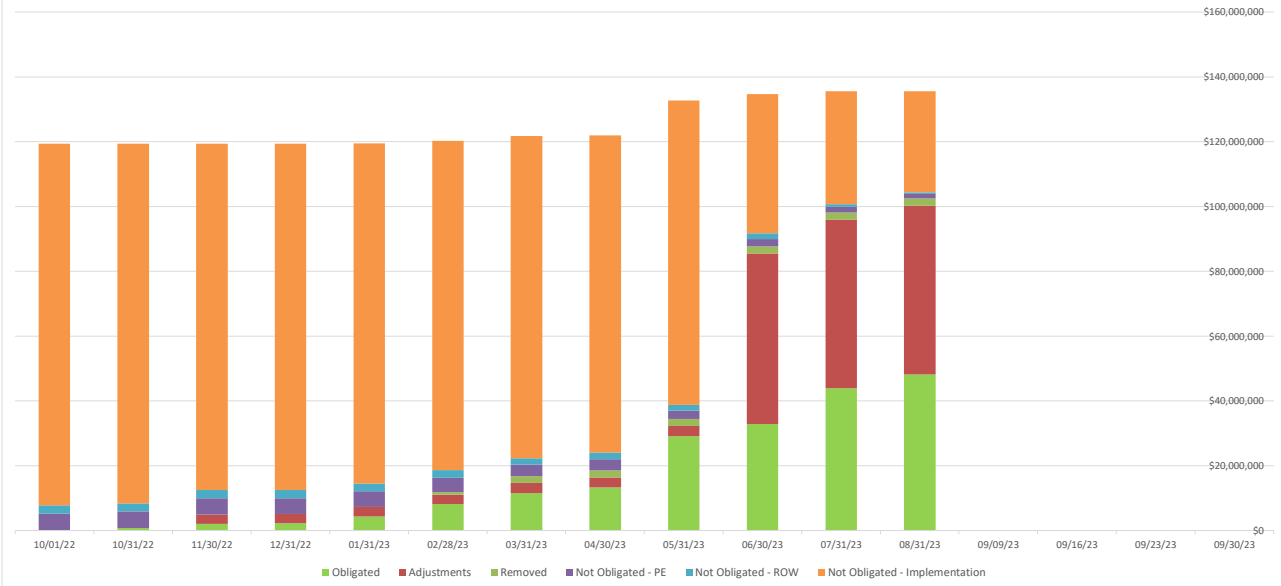

Date	Obligated		Adjustments		Removed		Not Obligated			Total				
	#	Federal \$	#	Federal \$	#	Federal \$	PE	ROW	CONST	#	Federal \$			
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23	52	\$29,210,065	7	\$3,097,069	2	\$2,160,000	17	\$2,577,687	20	\$1,771,206	79	\$93,923,975	177	\$132,740,002
06/30/23	62	\$32,935,192	43	\$52,596,382	2	\$2,160,000	15	\$2,352,167	20	\$1,771,006	41	\$42,910,827	183	\$134,725,574
07/31/23	83	\$43,955,847	46	\$52,050,562	3	\$2,215,200	8	\$1,755,390	11	\$758,384	33	\$34,907,151	184	\$135,642,534
08/31/23	94	\$48,253,136	46	\$52,050,562	3	\$2,215,200	6	\$1,377,578	7	\$502,384	28	\$31,243,674	184	\$135,642,534
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$48,253,136		94	PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/01/2022
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/05/2022
October Total			\$880,270		2	Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7133-23	\$1,224,000	CONST	Nov-22	11/30/2022
November Total			\$1,224,000		1	Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/2022
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/2022
December Total			\$216,000		2	Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Jul-23	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Sep-23	01/09/2023
January Total			\$2,130,892		5	Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Sep-23	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Dec-22	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
February Total			\$3,772,393		8	Projects
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Sep-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Jul-23	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
March Total			\$3,401,900		14	Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23	04/26/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jul-23	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brookling Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
April Total			\$1,712,714		3	Projects
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(A) - Replace Nine Vans	7232A-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(B) - Replace Nine Vans	7232B-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(A) - Replace Ten Buses	7232C-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(B) - Replace Ten Buses	7232D-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22	05/02/2023
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23	05/31/2023
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Jul-23	05/02/2023
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22	05/02/2023
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23	05/01/2023
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23	05/31/2023
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$349,065	CONST	Oct-24	05/09/2023
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22	05/30/2023
St. Charles	Zumbehl Rd - At Ipswich Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Apr-23	05/10/2023
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23	05/30/2023
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22	05/30/2023
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jul-23	05/18/2023
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23	05/30/2023
May Total			\$15,871,896		17	Projects
Arnold	Pomme Rd - Lonell Rd to Rockview Ln - Reconstruction, Sidewalk	7268-24	\$299,801	PE	Nov-23	06/15/2023
Bi-State Development/Metro	Wabash Station Planning - Planning For Future Uses at Wabash Station near Delmar MetroLink Station	7268-24	\$400,000	IMPL	Nov-23	06/01/2023

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$48,253,136		94	PROJECTS
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Sep-23	06/13/2023
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22	06/05/2023
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22	06/05/2023
St. Louis County	Dorsett Rd - 2026 - Marine to Calamaide - Resurfacing - Upgrade Sidewalks	7247B-24	\$289,500	PE	Nov-23	06/21/2023
St. Louis County	Hawkins Rd/New Sugar Creek Rd - Resurfacing, Shared Use Path	7247D-24	\$274,596	PE	Nov-23	06/28/2023
St. Louis County	Hanley Rd - 2026 - Dale Ave to Bruno Ave - Resurfacing, Sidewalk Upgrades	7247C-24	\$203,280	PE	Nov-23	06/01/2023
St. Louis County	Jennings Station/Chain of Rocks Rd - Halls Ferry Rd to St. Louis City Limit - Resurfacing, Shared Use Path, Upgrade Sidewalks	7247F-24	\$518,595	PE	Nov-22	06/21/2023
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22	06/20/2023
June Total			\$3,725,127		10	Projects
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23	07/05/2023
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23	07/13/2023
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23	07/25/2023
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Sep-23	07/27/2023
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22	07/15/2023
Jefferson County	Mt Olive Rd Bridge Over McMullen Branch - Replace Bridge	7113C-23	\$916,960	CONST	Oct-23	07/31/2023
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Sep-23	07/11/2023
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22	07/31/2023
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Sep-23	07/17/2023
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23	07/31/2023
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22	07/18/2023
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23	07/31/2023
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23	07/13/2023
St. Charles County	Zumbeh/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23	07/27/2023
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-23	07/31/2023
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22	07/27/2023
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22	07/31/2023
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Sep-23	07/17/2023
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23	07/17/2023
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22	07/24/2023
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23	07/12/2023
July Total			\$11,020,655		21	Projects
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood, 8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23	08/31/2023
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Sep-23	08/04/2023
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22	08/16/2023
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface - TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23	08/30/2023
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23	08/22/2023
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23	08/02/2023
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23	08/23/2023
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Sep-23	08/11/2023
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22	08/23/2023
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23	08/21/2023
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Sep-23	08/23/2023
August Total			\$4,297,289		11	Projects
September 8, 2023 Total			\$0		0	Projects
September 15, 2023 Total			\$0		0	Projects
September 22, 2023 Total			\$0		0	Projects
September 30, 2023 Total			\$0		0	Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$1,377,578	6 PROJECTS	
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$502,384	7 PROJECTS	
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
		TOTAL	\$31,243,674	28 PROJECTS	
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Sep-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Oct-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Sep-23
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Sep-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Sep-23
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Sep-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Sep-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Sep-23
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Sep-23
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Sep-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-23
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-23
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-23
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-23
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-23
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-23
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Sep-23

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$52,050,562	46 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2022
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23	EWG staff approved three-month schedule ext.	06/28/2023
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22	Board approved nine-month schedule ext.	06/28/2023
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22	EWG staff approved three-month schedule ext.	06/28/2023
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
June Total			\$48,180,993	35 Projects			
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23	MoDOT used ROW funds from 6S3416 - MoDOT resurfacing project on MO 115 - Shift ROW funds to construction	07/18/2023
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23	Coordination with adjacent MoDOT project design - shift ROW funds to construction	07/18/2023
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
July Total			\$772,500	4 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$2,215,200	3 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000	1 Project			
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000	1 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22	Project behind schedule	\$45,135
July Total			\$55,200	1 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2023 Reasonable Progress Update: July 31, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 184 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 50 different agencies and representing \$136 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

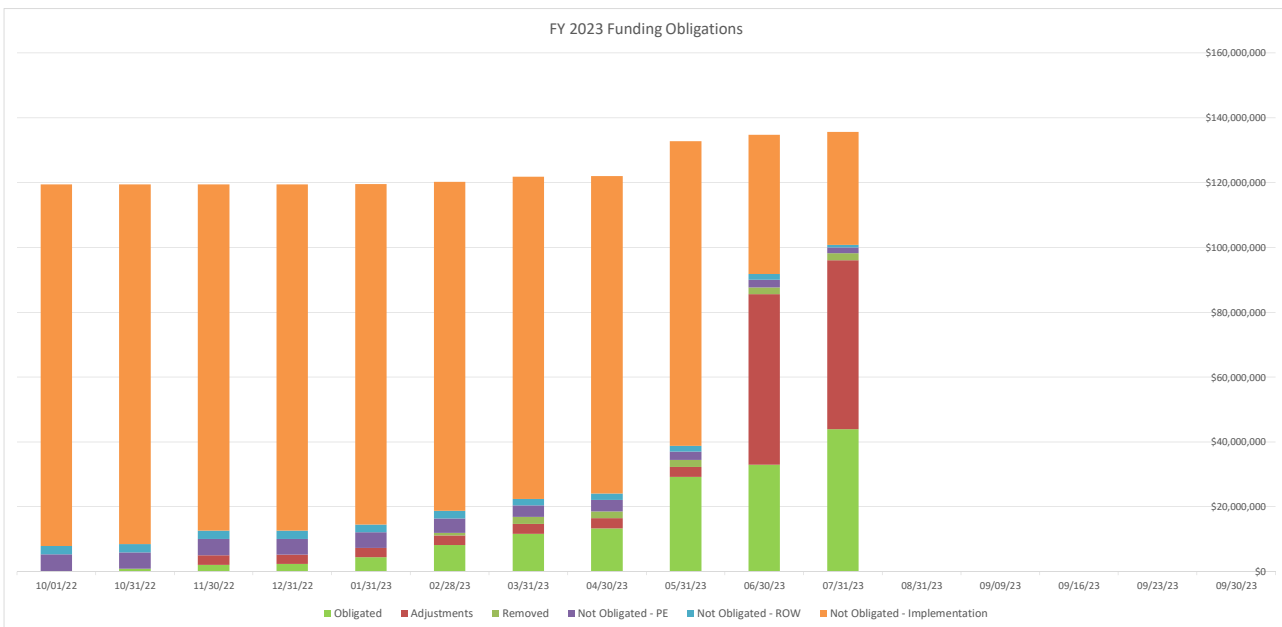

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23	52	\$29,210,065	7	\$3,097,069	2	\$2,160,000	17	\$2,577,687	20	\$1,771,206	79	\$93,923,975	177	\$132,740,002
06/30/23	62	\$32,935,192	43	\$52,596,382	2	\$2,160,000	15	\$2,352,167	20	\$1,771,006	41	\$42,910,827	183	\$134,725,574
07/31/23	83	\$43,955,847	46	\$52,050,562	3	\$2,215,200	8	\$1,755,390	11	\$758,384	33	\$34,907,151	184	\$135,642,534
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$43,955,847		83	PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/01/2022
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/05/2022
October Total			\$880,270		2	Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7183-23	\$1,224,000	CONST	Nov-22	11/30/2022
November Total			\$1,224,000		1	Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/2022
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/2022
December Total			\$216,000		2	Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Jul-23	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Sep-23	01/09/2023
January Total			\$2,130,892		5	Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Sep-23	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Dec-22	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
February Total			\$3,772,393		8	Projects
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Sep-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Jul-23	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
March Total			\$3,401,900		14	Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$437,298	CONST	Feb-23	04/26/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jul-23	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brookling Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
April Total			\$1,712,714		3	Projects
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(A) - Replace Nine Vans	7232A-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(B) - Replace Nine Vans	7232B-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(A) - Replace Ten Buses	7232C-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(B) - Replace Ten Buses	7232D-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22	05/02/2023
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23	05/31/2023
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Jul-23	05/02/2023
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22	05/02/2023
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23	05/01/2023
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23	05/31/2023
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$349,065	CONST	Oct-24	05/09/2023
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22	05/30/2023
St. Charles	Zumbel Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Apr-23	05/10/2023
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23	05/30/2023
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22	05/30/2023
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jul-23	05/18/2023
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23	05/30/2023
May Total			\$15,871,896		17	Projects

Obligated							
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation	
			TOTAL	\$43,955,847		83	PROJECTS
Arnold	Pomme Rd - Lonedell Rd to Rockview Ln - Reconstruction, Sidewalk	7268-24	\$299,801	PE	Nov-23	06/15/2023	
Bi-State Development/Metro	Wabash Station Planning - Planning For Future Uses at Wabash Station near Delmar MetroLink Station	7268-24	\$400,000	IMPL	Nov-23	06/01/2023	
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Sep-23	06/13/2023	
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22	06/05/2023	
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22	06/05/2023	
St. Louis County	Dorsett Rd - 2026 - Marine to Calamaide - Resurfacing - Upgrade Sidewalks	7247B-24	\$289,500	PE	Nov-23	06/21/2023	
St. Louis County	Hawkins Rd/New Sugar Creek Rd - Resurfacing, Shared Use Path	7247D-24	\$274,596	PE	Nov-23	06/28/2023	
St. Louis County	Hanley Rd - 2026 - Dale Ave to Bruno Ave - Resurfacing, Sidewalk Upgrades	7247C-24	\$203,280	PE	Nov-23	06/01/2023	
St. Louis County	Jennings Station/Chain of Rocks Rd - Halls Ferry Rd to St. Louis City Limit - Resurfacing, Shared Use Path, Upgrade Sidewalks	7247F-24	\$518,595	PE	Nov-22	06/21/2023	
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22	06/20/2023	
			June Total	\$3,725,127		10	Projects
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23	07/05/2023	
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23	07/13/2023	
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23	07/25/2023	
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Sep-23	07/27/2023	
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22	07/15/2023	
Jefferson County	Mt Olive Rd Bridge Over McMullen Branch - Replace Bridge	7113C-23	\$916,960	CONST	Oct-23	07/31/2023	
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Sep-23	07/11/2023	
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22	07/31/2023	
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Sep-23	07/17/2023	
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23	07/31/2023	
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22	07/18/2023	
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23	07/31/2023	
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23	07/13/2023	
St. Charles County	Zumbehl/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23	07/27/2023	
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5/3')	6905C-20	\$1,678,235	CONST	Sep-23	07/31/2023	
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22	07/27/2023	
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22	07/31/2023	
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Sep-23	07/17/2023	
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23	07/17/2023	
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22	07/24/2023	
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23	07/12/2023	
			July Total	\$11,020,655		21	Projects
			August Total	\$0		0	Projects
			September Total	\$0		0	Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$1,755,390	8 PROJECTS	
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface -TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$758,384	11 PROJECTS	
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$34,907,151	33 PROJECTS
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Sep-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Oct-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Sep-23
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Sep-23
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Sep-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Sep-23
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Sep-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Sep-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Sep-23
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Sep-23
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Sep-23
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Sep-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-23
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-23
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-23
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-23
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-23
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-23
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-23

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$34,907,151	33 PROJECTS
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Sep-23
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Sep-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$52,050,562	46 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2002
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23	EWG staff approved three-month schedule ext.	06/28/2023
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Franklin County	MO 47 - At Union Expy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22	Board approved nine-month schedule ext.	06/28/2023
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22	EWG staff approved three-month schedule ext.	06/28/2023
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
June Total			\$48,180,993	35 Projects			
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23	MoDOT used ROW funds from 6S3416 - MoDOT resurfacing project on MO 115 - Shift ROW funds to construction	07/18/2023
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23	Coordination with adjacent MoDOT project design - shift ROW funds to construction	07/18/2023
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23	Sponsor using local funds for ROW - preliminary plans submitted - Archeological study required	07/18/2023
July Total			\$772,500	4 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$2,215,200	3 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000	1 Project			
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000	1 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22	Project behind schedule	\$45,135
July Total			\$55,200	1 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2023 Reasonable Progress Update: June 30, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 183 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 50 different agencies and representing \$135 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

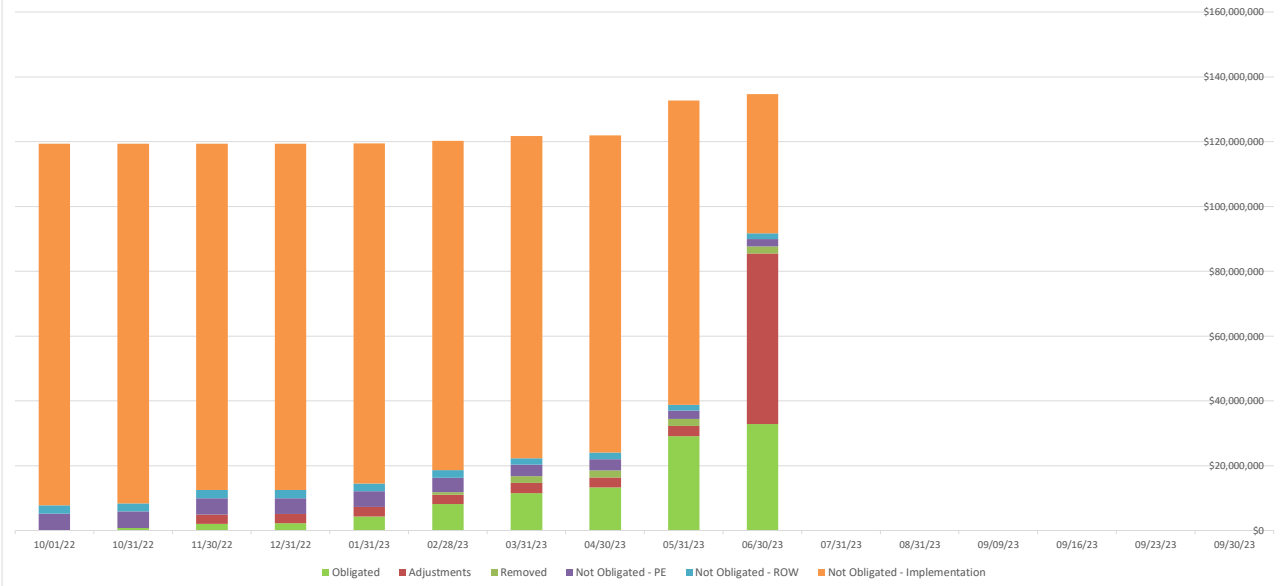

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	PE		ROW		CONST		#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23	52	\$29,210,065	7	\$3,097,069	2	\$2,160,000	17	\$2,577,687	20	\$1,771,206	79	\$93,923,975	177	\$132,740,002
06/30/23	62	\$32,935,192	43	\$52,596,382	2	\$2,160,000	15	\$2,352,167	20	\$1,771,006	41	\$42,910,827	183	\$134,725,574
07/31/23														
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$32,935,192		62 PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/01/2022
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/05/2022
			October Total	\$880,270		2 Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7183Z-23	\$1,224,000	CONST	Nov-22	11/30/2022
			November Total	\$1,224,000		1 Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/2022
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/2022
			December Total	\$216,000		2 Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Jul-23	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Sep-23	01/09/2023
			January Total	\$2,130,892		5 Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Sep-23	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Dec-22	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
			February Total	\$3,772,393		8 Projects
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Sep-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Jul-23	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
			March Total	\$3,401,900		14 Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23	04/26/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jul-23	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brookings Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
			April Total	\$1,712,714		3 Projects
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(A) - Replace Nine Vans	7232A-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(B) - Replace Nine Vans	7232B-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(A) - Replace Ten Buses	7232C-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(B) - Replace Ten Buses	7232D-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22	05/02/2023
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23	05/31/2023
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Jul-23	05/02/2023
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22	05/02/2023
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23	05/01/2023
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23	05/31/2023
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$349,065	CONST	Oct-24	05/09/2023
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22	05/30/2023
St. Charles	Zumbel Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Apr-23	05/10/2023
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23	05/30/2023
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22	05/30/2023
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jul-23	05/18/2023
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - W/park Dr to School	7200-23	\$183,230	PE	Mar-23	05/30/2023
			May Total	\$15,871,896		17 Projects
Arnold	Pomme Rd - Lonedell Rd to Rockview Ln - Reconstruction, Sidewalk	7268-24	\$299,801	PE	Nov-23	06/15/2023
Bi-State Development/Metro	Wabash Station Planning - Planning For Future Uses at Wabash Station near Delmar MetroLink Station	7268-24	\$400,000	IMPL	Nov-23	06/01/2023
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Sep-23	06/13/2023
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22	06/05/2023
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22	06/05/2023
St. Louis County	Dorsett Rd - 2026 - Marine to Calamaide - Resurfacing - Upgrade Sidewalks	7247B-24	\$289,500	PE	Nov-23	06/21/2023
St. Louis County	Hawkins Rd/New Sugar Creek Rd - Resurfacing, Shared Use Path	7247D-24	\$274,596	PE	Nov-23	06/28/2023
St. Louis County	Hanley Rd - 2026 - Dale Ave to Bruno Ave - Resurfacing, Sidewalk Upgrades	7247C-24	\$203,280	PE	Nov-23	06/01/2023
St. Louis County	Jennings Station/Chain of Rocks Rd - Halls Ferry Rd to St. Louis City Limit - Resurfacing, Shared Use Path, Upgrade Sidewalks	7247F-24	\$518,595	PE	Nov-22	06/21/2023
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22	06/20/2023
			June Total	\$3,725,127		10 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September Total	\$0		0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$2,352,167	15 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface -TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	Apr-23
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23
St. Charles County	Zumbehl/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL		\$1,771,006		20 PROJECTS	
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23
Pine Lawn	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$42,910,827	41 PROJECTS	
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Sep-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Oct-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Sep-23
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Sep-23
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Sep-23
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Sep-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Sep-23
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Sep-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Sep-23
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Sep-23
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Sep-23
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Sep-23
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Sep-23
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Sep-23
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Sep-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-23
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'/3')	6905C-20	\$1,678,235	CONST	Sep-23

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$42,910,827	41 PROJECTS	
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-23
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-23
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-23
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-23
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-23
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Sep-23
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Sep-23
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Sep-23
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$52,596,382	43 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2022
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23	EWG staff approved three-month schedule ext.	06/28/2023
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Franklin County	MO 47 - At Union Expyw - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22	Board approved nine-month schedule ext.	06/28/2023
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22	EWG staff approved three-month schedule ext.	06/28/2023
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23	Board approved nine-month schedule ext.	06/28/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22	EWG staff approved three-month schedule ext.	06/28/2023
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23	Board approved nine-month schedule ext.	06/28/2023
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23	Board approved nine-month schedule ext.	06/28/2023
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22	Board approved nine-month schedule ext.	06/28/2023
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22	Board approved nine-month schedule ext.	06/28/2023
June Total			\$49,499,313	36 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$2,160,000	2 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000	1 Project			
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000	1 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			


FY 2023 Reasonable Progress Update: May 31, 2023

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 170 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 50 different agencies and representing \$133 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

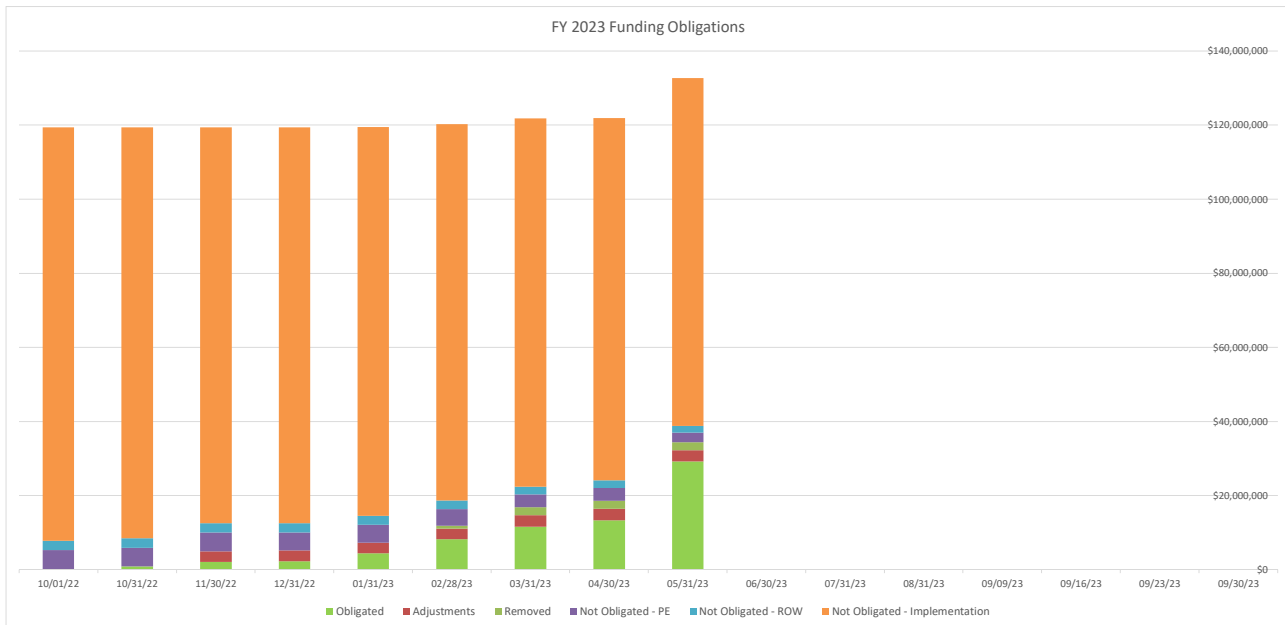

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23	52	\$29,210,065	7	\$3,097,069	2	\$2,160,000	17	\$2,577,687	20	\$1,771,206	79	\$93,923,975	177	\$132,740,002
06/30/23														
07/31/23														
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$29,210,065		52 PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/01/2022
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/05/2022
			October Total	\$880,270		2 Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7133-23	\$1,224,000	CONST	Nov-22	11/30/2022
			November Total	\$1,224,000		1 Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/2022
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/2022
			December Total	\$216,000		2 Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Jul-23	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Sep-23	01/09/2023
			January Total	\$2,130,892		5 Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Sep-23	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Dec-22	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
			February Total	\$3,772,393		8 Projects
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Sep-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Jul-23	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
			March Total	\$3,401,900		14 Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23	04/28/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jul-23	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brookling Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
			April Total	\$1,712,714		3 Projects
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(A) - Replace Nine Vans	7232A-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Call-a-Ride Vehicle Replacement - 2026(B) - Replace Nine Vans	7232B-26	\$1,028,484	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(A) - Replace Ten Buses	7232C-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Bi-State Development/Metro	Bus Replacement - 2025(B) - Replace Ten Buses	7232D-25	\$4,180,768	IMPL	Oct-25	05/01/2023
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22	05/02/2023
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23	05/31/2023
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Jul-23	05/02/2023
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22	05/02/2023
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23	05/01/2023
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23	05/31/2023
Shrewsbury	Weil/Wilhusen/St. Vincent - Weil: Shrewsbury-Wilhusen; Wilhusen: Weil-Lac. Stn - St. Vincent: Weil-Murdoch Cut-Off - Resurfacing	7124H-22	\$349,065	CONST	Oct-24	05/09/2023
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22	05/30/2023
St. Charles	Zumbehl Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Apr-23	05/10/2023
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23	05/30/2023
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22	05/30/2023
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jul-23	05/18/2023
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23	05/30/2023
			May Total	\$15,871,896		17 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September Total	\$0		0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$2,577,687	17 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface - TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	Apr-23
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23
St. Charles County	Zumbeh/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$1,771,006	20 PROJECTS	
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23
Pine Lawn	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$93,923,975	79 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Sep-23
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Oct-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Sep-23
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Sep-23
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Sep-23
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Sep-23
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Sep-23
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-22
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Sep-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$93,923,975	79 PROJECTS	
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Sep-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Sep-23
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Sep-23
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Sep-23
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Sep-23
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Sep-23
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Sep-23
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Sep-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-23
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$93,923,975	79 PROJECTS
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-23
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-23
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-23
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-23
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-23
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-23
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-23
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Sep-23
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Sep-23
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpont - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Sep-23
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL \$93,923,975 79 PROJECTS					
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$3,097,069	7 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2002
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$800,000		2 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
January Total			\$0		0 Projects		
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	69051-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000		1 Project		
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000		1 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2023 Reasonable Progress Update: April 30, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 172 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$122 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

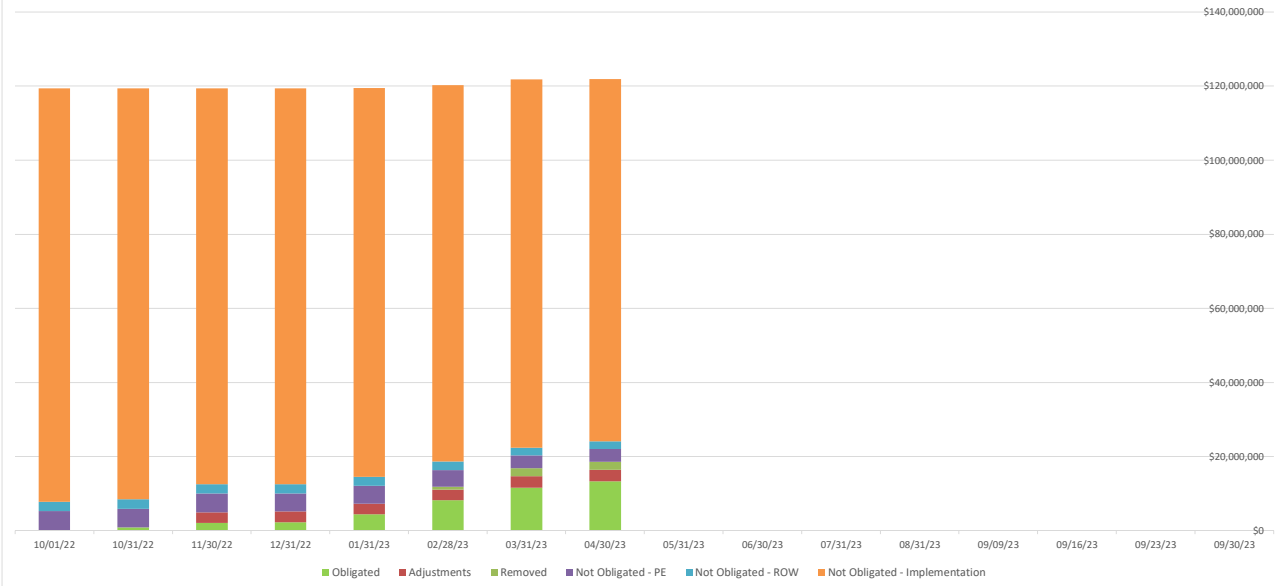

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23	32	\$11,625,455	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	87	\$99,420,166	171	\$121,832,393
04/30/23	35	\$13,338,169	7	\$3,097,069	2	\$2,160,000	22	\$3,502,697	21	\$2,027,006	85	\$97,847,292	172	\$121,972,233
05/31/23														
06/30/23														
07/31/23														
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$13,338,169			35 PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/1/22
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/5/22
October Total			\$880,270			2 Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7133-23	\$1,224,000	CONST	Nov-22	11/30/22
November Total			\$1,224,000			1 Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/22
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/22
December Total			\$216,000			2 Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Dec-21	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Dec-25	01/09/1923
January Total			\$2,130,892			5 Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Dec-24	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/22/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
February Total			\$3,772,393			8 Projects
Citizens For Modern Transit/BI-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Dec-23	03/15/2023
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23	03/16/2023
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23	09/09/2022
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23	06/15/2022
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23	03/15/2023
Jefferson County Port Authority	Marine Engine Repower - 2025 - Repower One Vessel	7254-25	\$1,499,000	IMPL	Sep-25	02/16/2023
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22	03/28/2023
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22	03/29/2023
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23	03/29/2023
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22	03/03/2023
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22	03/28/2023
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22	03/16/2023
St. Louis County	New Halls Ferry Rd Sidewalk - Lindbergh to Cougar Dr	7247G-24	\$62,000	PE	Oct-23	03/15/2023
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23	03/27/2023
March Total			\$3,401,900			14 Projects
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23	04/26/2023
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22	04/18/2023
St. Louis County	S. Woods Mill Rd - I-64 to Brooking Park Dr	7247I-24	\$139,840	PE	Oct-23	04/15/2023
April Total			\$1,712,714			3 Projects
May Total			\$0			0 Projects
June Total			\$0			0 Projects
July Total			\$0			0 Projects
August Total			\$0			0 Projects
September Total			\$0			0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$3,502,697	22 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface -TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23
St. Charles County	Zumbeh/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$2,027,006		21 PROJECTS
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23
Pine Lawn	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$97,847,292		85 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Sep-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Aug-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$97,847,292	85 PROJECTS
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Dec-21
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Jan-22
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Dec-22
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22
St. Charles	Zumbehl Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Oct-22
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$97,847,292	85 PROJECTS
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL \$97,847,292 85 PROJECTS					
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$3,097,069	7 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2002
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23	City will use local funds for PE	03/09/2023
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22	City will use local funds for PE	03/09/2023
March Total			\$207,328	2 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$800,000		2 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
January Total			\$0		0 Projects		
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	69051-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000		1 Project		
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22	Bridge adjacent to state park. Will require more environmental work	STP-4920(602)
March Total			\$1,360,000		1 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2023 Reasonable Progress Update: February 28, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 169 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$120 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations

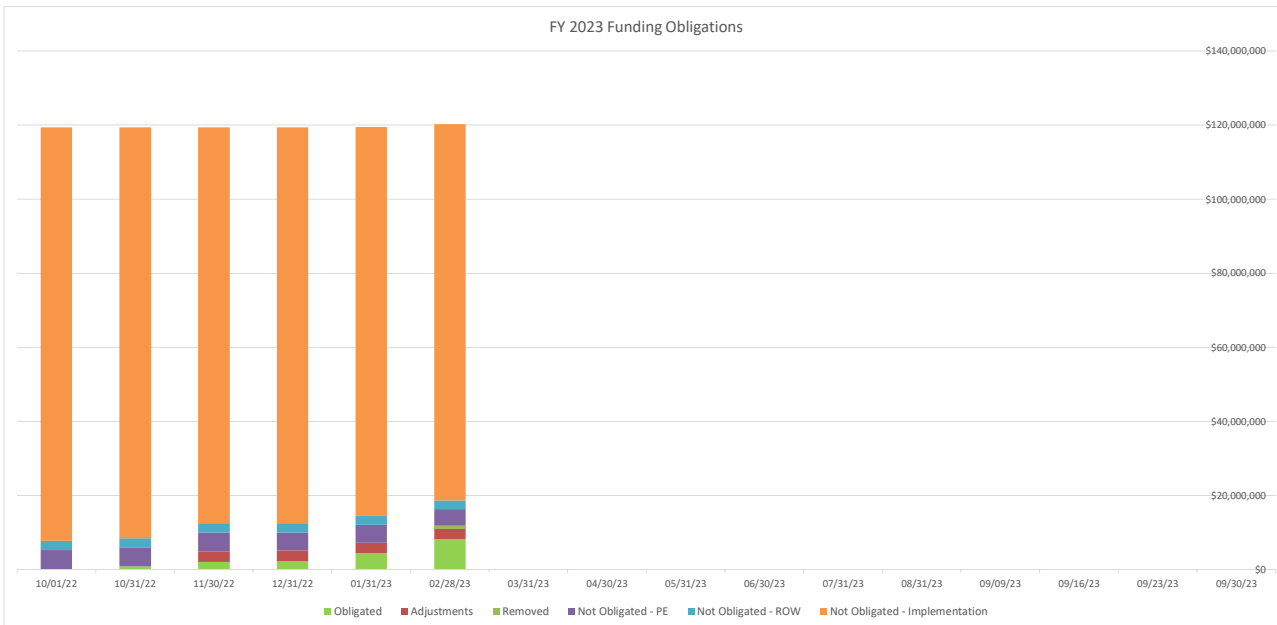

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,288,463	27	\$2,555,006	104	\$111,621,924	167	\$119,465,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,058,843	27	\$2,555,006	103	\$110,971,274	167	\$119,465,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,842,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
01/31/23	10	\$4,451,162	5	\$2,889,741	0	\$0	33	\$4,842,843	25	\$2,366,006	95	\$104,995,641	168	\$119,545,393
02/28/23	18	\$8,223,555	5	\$2,889,741	1	\$800,000	29	\$4,455,888	25	\$2,366,006	91	\$101,536,203	169	\$120,271,393
03/31/23														
04/30/23														
05/31/23														
06/30/23														
07/31/23														
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2022	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$8,223,555			18 PROJECTS
Franklin County	Hendricks Road Bridge - Over North Fork of Meramec River - Replace Bridge	6948-21	\$650,650	CONST	Dec-22	10/1/22
St. Louis County	Laclede Station Road - 2025 - Weil Ave to Watson Rd - Resurfacing - Curb Ramps	7196F-23	\$229,620	PE	Oct-22	10/5/22
October Total			\$880,270			2 Projects
MoDOT	MO 79 - At TR Hughes - Green T Intersection	7133-23	\$1,224,000	CONST	Nov-22	11/30/22
November Total			\$1,224,000			1 Projects
Maplewood	Greenwood Boulevard - Sussex Ave to Canterbury Ave - Reconstruction - Sidewalk (6-12')	7191-23	\$144,000	PE	Oct-22	12/12/22
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22	12/21/22
December Total			\$216,000			2 Projects
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Platin, Trib Hocom Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Dec-21	01/31/2023
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23	01/23/2023
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23	01/23/2023
Jefferson County	Old Highway M - Glenstone Dr to Chasteen Ln - Realignment	7187D-23	\$80,000	PE	Aug-23	01/23/2023
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Dec-25	01/09/1923
January Total			\$2,130,892			5 Projects
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23	02/28/2023
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22	02/02/2023
Jefferson County	Flucom Road - Hencher Rd to Athena Rd - Overlay, Shoulders	7187A-23	\$96,000	PE	Aug-23	02/07/2023
Loop Trolley TDD	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$1,260,000	CONST	Dec-24	02/03/2023
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23	02/28/2023
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21	02/01/2023
Washington	High Street - Fifth St to Front St - Resurfacing, Sidewalk	7199B-23	\$72,000	PE	Nov-22	11/30/22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22	02/01/2023
February Total			\$3,772,393			8 Projects
March Total			\$0			0 Projects
April Total			\$0			0 Projects
May Total			\$0			0 Projects
June Total			\$0			0 Projects
July Total			\$0			0 Projects
August Total			\$0			0 Projects
September Total			\$0			0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$4,455,888	29 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface -TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23
St. Charles County	Zumbel/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$2,366,006	25 PROJECTS	
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23
Pine Lawn	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$101,536,203	91 PROJECTS
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Dec-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Sep-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Aug-22
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
		TOTAL	\$101,536,203	91	PROJECTS
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Dec-21
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Jan-22
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	West Osage Street (Bl 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22
St. Charles	Zumbehl Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Oct-22
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$101,536,203	91 PROJECTS	
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$101,536,203	91 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$2,889,741	5 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2022
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$800,000		1 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
January Total			\$0		0 Projects		
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22	Additional time needed for ROW requirements	02/01/2023
February Total			\$800,000		1 Project		
March Total			\$0		0 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2023 Reasonable Progress Update: December 31, 2022

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 167 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2023 of the FY 2023-2026 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$120 million in federal funds, are subject to a September 30, 2023 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2023. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2023 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/22	0	\$0	0	\$0	0	\$0	36	\$5,424,463	27	\$2,555,006	104	\$111,621,924	167	\$119,601,393
10/31/22	2	\$880,270	0	\$0	0	\$0	35	\$5,194,843	27	\$2,555,006	103	\$110,971,274	167	\$119,601,393
11/30/22	3	\$2,104,270	5	\$2,889,741	0	\$0	35	\$5,058,843	27	\$2,555,006	97	\$106,857,533	167	\$119,465,393
12/31/22	5	\$2,320,270	5	\$2,889,741	0	\$0	33	\$4,706,843	27	\$2,555,006	97	\$106,857,533	167	\$119,329,393
01/31/23														
02/28/23														
03/31/23														
04/30/23														
05/31/23														
06/30/23														
07/31/23														
08/31/23														
09/09/23														
09/16/23														
09/23/23														
09/30/23														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
		TOTAL	\$4,842,843	33 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd - Intersection Realignment - Left Turn Lane	7231B-23	\$73,600	PE	Apr-23
Dardenne Prairie	Town Square Road - Winghaven Blvd to W City Limit (Near Technology) - Resurfacing	7234-23	\$67,839	PE	Oct-23
Dellwood	Hudson/Trask - Hudson: W. Florissant to Trask; Trask: Hudson to City Limits - Overlay	7178-23	\$68,235	PE	May-23
Ferguson	Robert Avenue - N. Florissant Rd to N. Elizabeth Ave - Reconstruct - Upgrade Sidewalks (5')	7179-23	\$124,721	PE	May-23
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$132,552	PE	Oct-22
Glendale	Sappington Road - Manchester Rd (MO 100) to Lockwood Ave - Resurfacing - Curb Ramps	7185-23	\$84,480	PE	Oct-22
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek - Replace Bridge	7187B-23	\$120,000	PE	Jan-23
Kirkwood	S. Clay Avenue - Adams Ave to Woodbine Ave - Raised Intersections - At Argonne/Jefferson Resurfacing - Upgrade Sidewalks (5')	7188A-23	\$111,200	PE	Nov-22
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave to BNSF RR - Resurfacing - Upgrade Sidewalks	7188B-23	\$114,320	PE	Nov-22
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing to 300' S/O Hawk Ridge Circle - Resurface - TWTL - Shared Use Path (10') - Sidewalk (5')	7235-23	\$175,000	PE	Apr-23
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd to Technology Dr Loop - Resurfacing - Sidewalk (6') - Shared Use Path (8')	7189-23	\$120,000	PE	Dec-22
Manchester	Hanna Road, Phase 2 - Brookvale Terrace to Big Bend Rd - Sidewalk Upgrade (5-6') - Overlay	7241-23	\$119,200	PE	Mar-23
MoDOT	MO 141 - At I-64 Interchange - Improvements to Off Ramps	7256-23	\$162,240	PE	Mar-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave to RR Tracks (S/O Civic Dr) - Resurfacing - Upgrade Sidewalks - TWTL	7192-23	\$137,600	PE	Sep-22
Pacific	Fourth Street - W. Osage St to Denton Rd - Resurfacing - Curb-Gutter - Upgrade Sidewalks (5')	7243-23	\$76,520	PE	Jun-23
St. Charles	Duchesne Drive - Droste Rd to W. Clay St - Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	PE	Oct-22
St. Charles	Muegge Road - Mexico Rd to Old Muegge Rd - Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$320,000	PE	Oct-22
St. Charles	2nd St Great Streets - Clark St to Bayard St - Upgrade Sidewalks (10') - Pervious Pavers	7244A-23	\$480,000	PE	
St. Charles County	Jungermann/Salt Lick/Spencer ATSPM - Jungermann: MO 364 to Boone H; Salt Lick I-70 to Span Trl - Spencer: Premier Pkwy to Willott Rd	7258A-23	\$143,360	PE	Apr-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P to Pitman St - Signal Optimization	7258B-23	\$14,232	PE	Mar-23
St. Charles County	Zumbahl/Elm/Fifth/Kingshwy ATSPM - Zum - I-70-Hawks Nest; Elm: Mueller-Elm Pt - Kingshwy: Clay-Elm; Fifth: Boones-Jeff	7258C-23	\$120,760	PE	Apr-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: DeBaliviere to Vandeventer - Fiber - Sidewalk - PTZ Cameras - Interconnection	7246B-23	\$400,000	PE	Apr-23
St. Louis County	Milburn Road - At Yaeger Rd - Roundabout - Sidewalks	7247J-23	\$169,260	PE	Oct-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber - Sidewalk - Queensbrooke to Sugarwood	7259-23	\$63,022	PE	Apr-23
St. Peters	Barkwood Trails Drive - Jungermann Rd to Maple Tree Dr - Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$202,812	PE	Dec-22
St. Peters	Jungs Station Road - Kings Crossing to Country Mill Ct - Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$182,804	PE	Dec-22
St. Peters	Mexico Road Bridge - At Dardenne Creek - Bridge Rehabilitation	7197C-23	\$52,265	PE	Dec-22
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd to Weber Hill Rd - Resurfacing - Sidewalk (5')	7248-23	\$136,000	PE	Dec-22
University City	Kempland Place Bridge - Over River Des Peres - Rehabilitate Bridge	7249-23	\$76,480	PE	Jun-23
University City	Pershing Avenue - Linden to Forest Park Pkwy - Linden to N Hanley Local Funds - Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$130,848	PE	Oct-22
Washington	Front Street, Phase 2 - Stafford St to Jefferson St - Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$72,000	PE	Oct-22
Wentzville	Pearce Blvd - At Linn Ave - Traffic Signal	7260-23	\$48,263	PE	Feb-23
Wentzville	Mexico Road - Josephville Rd to Midland Park Dr - Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr to School	7200-23	\$183,230	PE	Mar-23

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$2,555,006	27 PROJECTS	
Creve Coeur	US 67 - At Old Olive Street Rd - Intersection Improvements - Bike/Ped Xing	7106-23	\$256,000	ROW	Oct-22
Des Peres	Lindemann Road - Manhattan Ave to Kirkwood City Limits (S/O Lillian Ave) - Resurfacing - Sidewalk (6')	7108-22	\$28,000	ROW	Feb-23
Florissant	Rue St. Denis, Phase 2 - N. Lafayette St to N. New Florissant Rd - Resurfacing - Sidewalk (5-6')	7111-22	\$55,200	ROW	Oct-22
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd to Huntleigh Trails Ln - Resurfacing - Sidewalk (6')	7112-22	\$187,700	ROW	Oct-22
Frontenac	Spoede Road Bridge - Over Deer Creek - Replace Bridge - Sidewalk (6')	7184-23	\$12,000	ROW	Mar-23
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd to Dellwood Ln - Resurfacing - Restripe for TWTL - Shared Use Path (8')	7113A-23	\$31,500	ROW	Aug-23
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd to Spring Forest Rd - Reconstruction - Shoulders (5')	7113B-23	\$111,000	ROW	Aug-23
Jefferson County	Dulin Creek Road - Meyer Ln to Local Hillsboro Rd - Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$100,000	ROW	Aug-23
Jefferson County	Saline Road - Northwest Blvd to 400' S/O Memory Ln - Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$157,500	ROW	Aug-23
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave to Adams Ave - Resurfacing - Upgrade Sidewalks	7114-22	\$94,184	ROW	Oct-22
Kirkwood	Lindemann Road - Dougherty Ferry Rd to Des Peres Limit (120' S/O Montour) - Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$100,000	ROW	Oct-22
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy to Spillway Bridge - Sidewalks (6')	7159-22	\$52,500	ROW	Dec-22
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr to Valleybrook Dr - Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$30,000	ROW	Aug-22
O'Fallon	Main Street, Phase 2 - Pitman St to Terra Rd - Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$120,000	ROW	Jun-23
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy to Barat Haven Blvd - Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$6,500	ROW	Mar-23
Pacific	Osage St - At First Street - Add Right Turn Lane - Intersection Improvements	7210-22	\$120,000	ROW	Feb-23
Pine Lawn	Natural Bridge (MO 115) Sidewalks - Dardenne Ave to Avondale Ave - Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$16,000	ROW	Apr-23
St. Charles	Second Street - First Capitol Dr to Boones Lick Rd - Reconstruction - Upgrade Sidewalks (5')	7120-22	\$80,000	ROW	Feb-23
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm - Sidewalk (5-6')	7164-22	\$24,000	ROW	Feb-23
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek - Replace Reavis Barracks Bridge - Realign Grenn Park Rd to Reavis Barracks Rd	7124G-22	\$630,000	ROW	Sep-23
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance to Cedar Crest Creek Dr - Sidewalk (5')	7167-22	\$120,000	ROW	Jul-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd - Turn Lanes - Upgrade Traffic Signal	7212-22	\$32,000	ROW	May-23
University City	Canton Avenue, Phase 2 - Midland Blvd to Pennsylvania Ave - Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$36,000	ROW	Oct-22
Wentzville	Wentzville Parkway - Meyer Rd to Parkway Ridge Blvd - Reconstruct - TWTL (Locally Funded) - Shared Use Path (10')	7127-23	\$32,522	ROW	Oct-22
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd to Veterans Memorial Pkwy - Sidewalk (6')	7168-22	\$2,400	ROW	Jun-23
Wildwood	MO 109 - At MO BA (South) - Roundabout - Shared Use Path (10')	7129-22	\$40,000	ROW	Dec-22
Wildwood	Old State Road Shared Use Path - Old State Place Dr to Nantucket Island Dr - Shared Use Path (10') - Connection to Waterfront Way	7169-22	\$80,000	ROW	Oct-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$106,857,533	97 PROJECTS	
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust - Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jan-23
Brentwood	Deer Creek Greenway Connector - Brentwood: Marshall-Brazeau; Russell-Brentwood-Bremerton - Shared Use Path (12' Brentwood,8' Russell), Sidewalk	7154-22	\$932,000	CONST	Feb-23
Citizens For Modern Transit/Bi-State	Building Transit Ridership - STL City and STL County - Education & Outreach - Employer Outreach Two Year Program	7253-23	\$275,049	CONST	Dec-23
Clayton	Bonhomme Ave & Meramec Ave - Bonhomme: Brentwood-Hanley; Meramec: Shaw Park Dr to Maryland Ave - Resurfacing - Curb Ramps	6915-22	\$965,535	CONST	Nov-21
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	May-23
Creve Coeur	New Ballas Road, Phase 1 - Olive Blvd to Craig Rd - Slab Replacement - Diamond Grind - Repl. Sidewalk (5')	6940-22	\$816,000	CONST	Sep-22
Dardenne Prairie	Stump Road - Feise Rd to MO N - Reconstruction - Sidewalks (5') - Left Turn Ln	6941-21	\$828,320	CONST	Oct-22
De Soto	N. Main Street, Phase 2 - Valley Pl to Williams St - Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Dec-22
De Soto	Boyd Street Sidewalk - MO 21 to Thomas St - Sidewalk (6')	7156-22	\$286,304	CONST	Mar-22
Edmundson	Edmundson Road - Natural Bridge to Holman Ln - Resurfacing - Sidewalk (6') - Lighting	6943-22	\$557,428	CONST	Dec-21
Fenton	Larkin Williams Road - South Highway Dr to Wolfner Dr - Whitetopping - Sidewalk (5')	6944-21	\$1,156,890	CONST	Oct-22
Ferguson	S. Dade Avenue - Airport Rd to Suburban Ave - Resurfacing - Curb Ramps	6945-21	\$457,298	CONST	Feb-23
Festus	W. Main Street, Phase 1 - Park Ave to Mill St - Resurfacing - Sidewalks (6') - Lighting	6946-22	\$623,052	CONST	Dec-21
Festus	W. Main Street, Phase 2 - Hancock Ct to Park Ave - Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Dec-22
Florissant	Rue St Denis, Phase 1 - St. Ferdinand St to N. Lafayette St - Resurfacing - Sidewalk (5-6')	6921-20	\$895,200	CONST	Oct-21
Franklin County	MO 47 - At Union Expwy - Roundabout	7125B-23	\$1,318,912	CONST	Dec-22
Franklin County	Little Indian Creek Road Bridge - Over Girard Branch of India - Replace Bridge - Shoulders (2')	7182B-23	\$538,419	CONST	Dec-23
Frontenac	Geyer Road, Phase 1 - Clayton Rd to Hermitage Hill Rd - Resurfacing - Sidewalk (6') - Storm Sewer	6899-20	\$862,400	CONST	Oct-21
Glendale	E. Essex Avenue - Sappington Rd to Dickson St - Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Feb-23
Great Rivers Greenway	Maline Greenway - Ted Jones Trail to W. Florissant Ave - Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Nov-22
Hazelwood	Phantom Drive - Missouri Bottom Rd to James S. McDonnell Blvd - Lane Reduction 4 to 2 Lanes - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Oct-21
Jefferson County	Armbruster, Doss Hollow, Harness Bridges - Over Haverstick, Plattin, Trib Hocum Hollow Creeks - Replace Bridge	6913A-20	\$1,492,467	CONST	Dec-21
Jefferson County	Seckman Road - At Mastodon State Park - Realign Intersection - Left Turn Lane - Shoulders (8')	6913E-20	\$626,500	CONST	Dec-21
Jefferson County	Allen Road Bridge - Over Sandy Creek - Replace Bridge	6952A-21	\$964,800	CONST	Dec-22
Jefferson County	Hunning Road - Elizabeth Ln to Approx. 300' N/O Cinphany Ct - Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Dec-22
Jefferson County	Laguna Palma Road & McGehan Road Bridges - Over Boyd Branch & Tributary of Joachim Creek - Replace Bridges	6952C-21	\$1,377,600	CONST	Dec-22
Jefferson County	Old Lemay Ferry Road - 0.42 Mi. S/O Regency Woods Pl to Kneff Rd - Safety Improvements - Shoulders (4') - High Friction Treatment	6952E-21	\$1,322,376	CONST	Jan-23
Jefferson County	Seckman Road, Phase 2 - 700' W/O Outer Rd to 400' E/O Mastodon Park Ent. - Shoulder (8') - Overlay - Curb & Gutter - Safety Impr.	6952G-21	\$872,998	CONST	Dec-22
Jefferson County Port Authority	Marine Vessel Engine Repower - 2023 - Repower Two Marine Vessels Serving Mississippi River in Non-Attainment Area	7205-23	\$408,144	CONST	Dec-22
Kirkwood	Geyer Road, Phase 2 - West Adams Ave to 50' N/O Big Bend Rd - Resurfacing - Curb Ramps - Reconstruct road at UP RRxing	6917-22	\$1,139,635	CONST	Aug-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
TOTAL			\$106,857,533	97 PROJECTS	
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) to Geyer Rd - Reconstruction - Replace Sidewalks (5') - Bike Lane	6953-22	\$1,304,000	CONST	Oct-22
Ladue	Dielman Road - Tamarack Dr to Ladue Rd - Resurfacing - Sidewalk (5')	6954-22	\$916,729	CONST	Oct-22
Lake Saint Louis	Hawkridge Trail/Sommers Road - At Old Highway N - Traffic Signal	7131-22	\$503,000	CONST	Dec-22
Lake Saint Louis	Flashing Yellow Arrows & Signal Improvements - Along Ronald Reagan Dr, Technology Dr, Lake Saint Louis Blvd - Upgrade Signal Controllers	7206-22	\$265,282	CONST	Mar-23
Lake Saint Louis	Ronald Reagan Drive & Hawks Ridge Trail - Reagan: I-64-MO N; Hawks Ridge: Ridgeway-MO N - Resurfacing - Sidewalks (5')	6901-20	\$1,115,576	CONST	Jan-22
Lake Saint Louis	Old Highway N - 125' S/O Hawk Ridge Trail to 50' S/O Old Forester Dr - Reconstruct - Sidewalk (6') - TWTL (Locally Funded)	7101B-22	\$805,000	CONST	Dec-22
Loop Trolley Tdd	Loop Trolley Operating Assistance - Funding for Two Years	7255-23	\$630,000	CONST	Dec-24
Manchester	La Bonne Parkway - Big Bend Rd to Carman Rd - Reconstruction - Upgrade Sidewalks (5')	7116-23	\$1,098,740	CONST	Dec-22
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd to MO 141 - Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Sep-23
Maryland Heights	Adie Road - US 67 (Lindbergh Blvd) to Dorsett Rd - Reconstruction - Sidewalks (5') - Replace Culvert	6956-23	\$820,000	CONST	Feb-23
MoDOT	MO 109 - At MO CC (Wild Horse Creek Rd)/S. Eatherton Rd - Roundabout	6979B-20	\$2,116,000	CONST	Jul-22
MoDOT	Signal Optimization - 2023 - MO 231: Hoffmeister to US 67; US 67: MO 231 to I-55 -	7134-23	\$957,008	CONST	Jan-23
MoDOT/American Lung Association	St. Louis Regional Clean Air Partnership - Metro St. Louis Area - Outreach - Education - Promotion of Gateway Guide - Ozone Alert	7257-23	\$369,425	CONST	Dec-25
New Haven	New Haven Middle School Shared Use Path - New Haven Park Trail to Middle School - Shared Use Path (10')	7160-22	\$156,263	CONST	Mar-23
O'Fallon	Main St, Phase 1 - Pitman St to S/O Railroad Tracks - Resurfacing - Curb Ramps - Sidewalks	6904-20	\$1,763,679	CONST	Dec-21
Olivette	Centennial Greenway, Phase 1 - Warson Park to Dielman Rd - Shared Use Path (10-12')	7162-22	\$1,000,000	CONST	Jan-22
Pacific	Congress St (Former Rte N) - Westlake Village Dr to Candlewick Ln - Resurfacing - Lighting - Storm Sewer - Bike Lane (5')	6959-21	\$784,271	CONST	Dec-22
Pacific	West Osage Street (BI 44) - Noonan Plaza to I-44 Off Ramp; Western Ave to Viaduct St - Sidewalk (5')	7163-22	\$215,706	CONST	Apr-22
St. Charles	SCAT Transit Parking Under I-70 - Under I-70 at S. Main Street - Bus Stop-Bike Path - Construct Parking Lot (25 Spots for Transit Park & Ride)	7135-23	\$424,000	CONST	Oct-22
St. Charles	Zumbel Rd - At Ipswitch Ln - Traffic Signal - Turn Lanes	7136-23	\$250,000	CONST	Oct-22
St. Charles	S. Fifth Street - Fairgrounds Rd to San Juan Dr - Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Mar-23
St. Charles County	GGL - Mid Rivers Mall Dr Signal Performance Module - I-70 North Outer Rd to S St. Peters Pkwy - Automated Traffic Signal Perf. - Signal Optimization	7137A-21	\$1,358,400	CONST	Oct-22
St. Charles County	GGL - Bryan Rd & Wentzville Pkwy Signal Perf. Module - Bryan: W. Terra Ln to MO N; WP Veterans Mem Pkwy to US 61 - Automated Traffic Signal Perf. - Signal Optimization	7137B-21	\$1,761,400	CONST	Dec-21
St. Charles County	GGL - Muegge Rd Signal Performance Module - Cave Springs Rd to Old 94 - Automated Traffic Signal Perf. - Signal Optimization	7211B-22	\$785,403	CONST	Mar-23
St. Charles County	Gutermuth Road, Phase 3 - Old Gutermuth Rd to Motherhead Rd - Reconstruction - Sidewalks (5') TWTL (Locally Funded)	6923-22	\$1,020,000	CONST	Oct-21
St. Charles County	Interstate Drive - Prospect Rd to E/O Quail Ridge Park Ent. - Reconstruction - Shoulder (6') - Sidewalk (5')	6961-22	\$900,000	CONST	Dec-21
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,000,000	CONST	Oct-22
St. Louis	Sulphur Ave Bridge - Over River Des Peres - Replace Bridge Deck, Bridge Rehab	5205C-17	\$236,000	CONST	Sep-22
St. Louis	Traffic Management Enhancements, Phase 4 - Various locations along Goodfellow, MLK Dr, Halls Ferry Rd - Traffic Monitoring Cameras - Signal Impr.	6982B-20	\$2,580,000	CONST	Dec-21
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grove/Vandeventer: Laclede-Mag - Cycle Track - Tower Grove/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Oct-22

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
			TOTAL	\$106,857,533	97 PROJECTS
St. Louis	Tucker Boulevard Cycle Track - Washington Ave to Chouteau Ave (MO 100) - Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jan-23
St. Louis	20th Street - Market St to St. Louis Ave - Cycletrack - Traf. Signals - Shared Use Path - Lighting - Sidewalk - Signal Intercnt	6982A-20	\$5,000,000	CONST	Sep-22
St. Louis County	S. Woods Mill - At Conway - Intersection Improvements - Turn Lanes - Traffic Signal	7139-21	\$498,160	CONST	Sep-23
St. Louis County	Mason Road - 2022 - Clayton Rd to 100' N/O Mason Ridge Rd - Resurfacing - Shared Use Path (8') - Curb Ramps	6905A-20	\$1,318,320	CONST	Sep-22
St. Louis County	J.S. McDonnell Blvd Bridge - Over Coldwater Creek - Replace Bridge - Shoulder (5'3')	6905C-20	\$1,678,235	CONST	Sep-22
St. Louis County	Chesterfield Pkwy West (South) - 2022 - I-64 to Clarkson Rd - Resurfacing - Curb Ramps	6905D-22	\$1,100,000	CONST	Sep-22
St. Louis County	Kingsland Avenue - 2022 - Vernon to Delmar Blvd - Resurfacing - Curb Ramps	6905E-20	\$708,852	CONST	Sep-22
St. Louis County	Midland Blvd (East) - 2022 - Woodson Rd to North & South Rd - Resurfacing - Curb Ramps	6905F-22	\$1,600,000	CONST	Sep-22
St. Louis County	N. Elizabeth Avenue- 2022 - Pershall Rd to Chambers Rd - Resurfacing - Curb Ramps	6905G-22	\$800,000	CONST	Sep-22
St. Louis County	New Ballwin Road - 2022 - Twigwood Dr to Oak Leaf Manor Ct - Resurfacing - Curb Ramps	6905H-22	\$800,000	CONST	Sep-22
St. Louis County	Vernon Avenue - 2022 - Midland Blvd to City of St. Louis Line - Resurfacing - Curb Ramps	6905I-22	\$800,000	CONST	Sep-22
St. Louis County	Weidman Road - 2022 - Turtle Cove Dr to Manchester Rd (Mo 100) - Resurfacing - Curb Ramps	6905J-22	\$800,000	CONST	Sep-22
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd to E. Lockwood Ave - Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Sep-23
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) to Couch Ave - Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Sep-23
St. Louis County	Craig Road - 2023 - Lackland Rd to Olive Blvd (Mo 340) - Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Sep-23
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) to Page Ave (MO D) - Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Sep-23
St. Louis County	McKelvey Road - 2023 - Natural Bridge Rd to I-270 - Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Sep-23
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) to Canton Ave - Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Sep-23
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) to Washington St - Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Sep-23
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers to Bermuda - Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Sep-23
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd to W/O MO 367 - Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Sep-23
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting - Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Sep-23
St. Peters	Spencer Road - Thoele Rd/Springwood Dr to Willot Rd - Reconstruction - Mini Roundabouts - Sidewalk (6')	6965-23	\$1,207,340	CONST	Dec-22
Sunset Hills	West Watson Road - Gravois Rd (MO 30) to Weber Hill Rd - Resurfacing - Shared Use Path (10') - Sidewalk (5')	6966-21	\$854,560	CONST	Aug-23
Union	N. Oak Street - E. Springfield Ave to US 50 - Resurfacing - Sidewalks (6-10')	6968-22	\$309,249	CONST	Dec-21
Union	Union Expressway - MO 47/US 50 to MO 47/Old Country Farm Rd - New Road	7125A-23	\$6,936,406	CONST	Dec-22
Valley Park	St. Louis Avenue/Beckett/Marshall, Phase 3 - MO 141 to 3rd St - Reconstruct: RR to 3rd; Resurf: RR to 141 - Sidewalks (5')	6918-20	\$1,308,553	CONST	Aug-22
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - N/S: Page to Midland; Midland: N/S to Delpport - Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jan-23
Washington	Third Street - MO 47 to Jefferson St - Resurfacing - Sidewalk (5')	6910-20	\$678,392	CONST	Jan-22
Washington	Jefferson Street - Fifth St to MO 100 - Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Oct-22
Washington	Westlink Drive - Bluff Rd to W. Main St. - Overlay - Improve Intersection at Bluff Rd	6971-21	\$374,200	CONST	Oct-22

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation
		TOTAL	\$106,857,533	97 PROJECTS	
Wentzville	MO Z - At Interstate Dr - Add NB Right Turn Lane	6984-20	\$138,327	CONST	Jan-22
Wentzville	MO Z - At Interstate Dr - Restripe MO Z Int. Dr to 70 (Loc. Fund) - Upgrade Traffic Signal - Intersection Improvements	7140-21	\$998,783	CONST	Feb-23
Wentzville	Peine Road - 60' E/O Forest Way Dr to 675' W/O Stewart Springs Dr - Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Dec-22
Wentzville	W. Pearce (I-70 N. Outer Rd) - May Rd to 200' W/O Faith Church Ent. - Resurfacing - Shoulders (2') - Fencing	6973-21	\$1,009,438	CONST	Oct-22
Wildwood	Wild Horse Creek Road Bridge - Over Wild Horse Creek - Replace Bridge	6974-23	\$1,360,000	CONST	Nov-22
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St - Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Dec-22

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$2,889,741	5 PROJECTS			
October Total			\$0	0 Projects			
Franklin County	Huff Road Bridge - Over Tributary Of Pierce Creek - Replace Bridge	5187B-23	\$557,418	CONST		County BRO not tracked	11/30/2022
Franklin County	Lockhart Road Bridge - Over Logan Branch - Replace Bridge	5187C-23	\$530,763	CONST		County BRO not tracked	11/30/2022
Jefferson County	Antire Road - 400' N/O Crestview Dr to 200' E/O Sunshine Dr - Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	Technical correction - construction funding in FY 24 per application	11/30/2022
St. Louis County	Hudson Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204D-19	\$449,640	CONST		County BRO not tracked	11/30/2022
St. Louis County	Vorhof Dr Bridge - Over Black Jack Creek - Bridge Rehabilitation	5204F-19	\$434,920	CONST		County BRO not tracked	11/30/2022
November Total			\$2,889,741	5 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			
